06/29/00 11:10 FAX 303 293 223

2001 M/023/007

NORTH LILY MINING COMPANY

1800 Glenarm Place #210 Denver, Colorado, 80202

> (303)-294-0427 (303)-293-2235

Beginning to send 07 pages (including cover sheet) if transmission is interrupted or of poor quality, please notify us immediately by calling 303-294-0427.

DATE:

29 June 2000

TO:

Mary Ann Wright

Assoc. Director

FAX:

801-359-3940

FROM:

Gene Webb/Steve Flechner

RE:

Reclamation Plan Timetable

Attached is revised timetable. As discussed, we intend to fund with land sales, if funding not timely available from corporate financing.

Attached for your information are a map identifying our 8,000 acres of Utah property (which include about 400 acres at the Silver City project), and a summary sheet appraising 890 acres at \$864,000 (parcel A), and informally valuing the nearby comparable 800 acres at \$776,000 (parcel B).

Regards,

This facsimile message and/or document is legally privileged and confidential information intended only for the use of the individual or entity named above. If the reader of this message is not the intended recipient, you are hereby notified that any dissemination. distribution or copying of this telecopy is strictly prohibited. If you have received this telecopy in error, please immediately notify us by telephone and return the original message to us at the address above via the United States Postal Service. Thank you.

nlmcfaxe




Proposed Reclamation and Closure Schedule for 2000 Revised 6-29-00				
	Component		Start Date	Anticipated Completion Date
1.	Restore Pad Perimeter Solution Collection System		May 8	May 9 (completed)
2.	2.1 2.2 2.3 2.4 2.5 2.6 2.7	& Start up Enhanced Evaporation System Design Schematic Solution Channel Liner Repairs Reinstall ADS pipe underdrain in pad solution channel. Site Clean-up Flow meter and weir or flume * Install new pump* Install and Start-up Pad Margin Evap. System Relocate Evap. Away from margin	May 22	July 10 April 28 (completed) Not needed August 11 August 11 July 21 Completed back-up only Abandoned Completed
	2.9 Assessment 2.10 2.11 2.12 2.13	Install Overflow Pond Evap, if needed** Review & Schedule Readjustment Repair Pregnant Pond Liner Reestablish Pregnant Pond Leak Detection System Construct, Install In-pond Evap. System. Estimate Post-Closure Draindown	July 10 May 16 July 5 ** July 21 ** July 17 ** August 14	July 21 Completed July 21 ** July 28 ** August 5 August 21
3.	Design Post- 3.1 3.2	Closure Fluid Management System Conceptual Design Final Design	April 15 August 30	August 18 September 22

Proposed Reclamation and Closure Schedule for 2000 Revised 6-29-00				
	Component	Start Date	Anticipated Completion Date	
4.	Characterize, Identify, and Quantify Stockpile	July 17	September 6	
	Topsoil & Topsoil Substitute, Finalize Seed Mix 4.1 Nutrient characterization of stockpiled topsoil and estimate	July 17	August 31	
	stockpile volume 4.2 Determine topsoil thickness	July 17	September 6	
	requirements 4.3 Identify source of topsoil substitute and perform nutrient characterization	July 17	September 6	
	Assessment Review & Schedule Readjustment 4.4 Finalize seed mix	June 15 July 17	Completed September 6	
5.	Assess Adequacy of Natural Revegetation in Former Land Application Areas (to be done by DOGM)	June 1	July 21	
Assı	essment Review and Schedule Readjustment	July 13		
6.	Regrade Heap Leach Pad	September 11	September 15	
	essment Review & Schedule Readjustment Date	August 15		
7.	Apply Topsoil	September 18	October 15	
8.	Apply Seed and Soil Amendments	October 15	November 15	
9.	Inventory and Dispose of Salvageable, Recyclable, and Unusable Materials			
	9.1 Inventory 9.2 Disposal	July 10 July 30	July 30 November 30	
On-site Review		December 5 (on or before)		
10.	Construct Post-Closure Fluid Management System	November 1	December 31	
11.	10.5.	September 30	December 31	

^{*} Pending equipment availability.

^{**} Dependent upon results of previous components and/or agency approvals.

All above are dependent upon timely availability of funding.

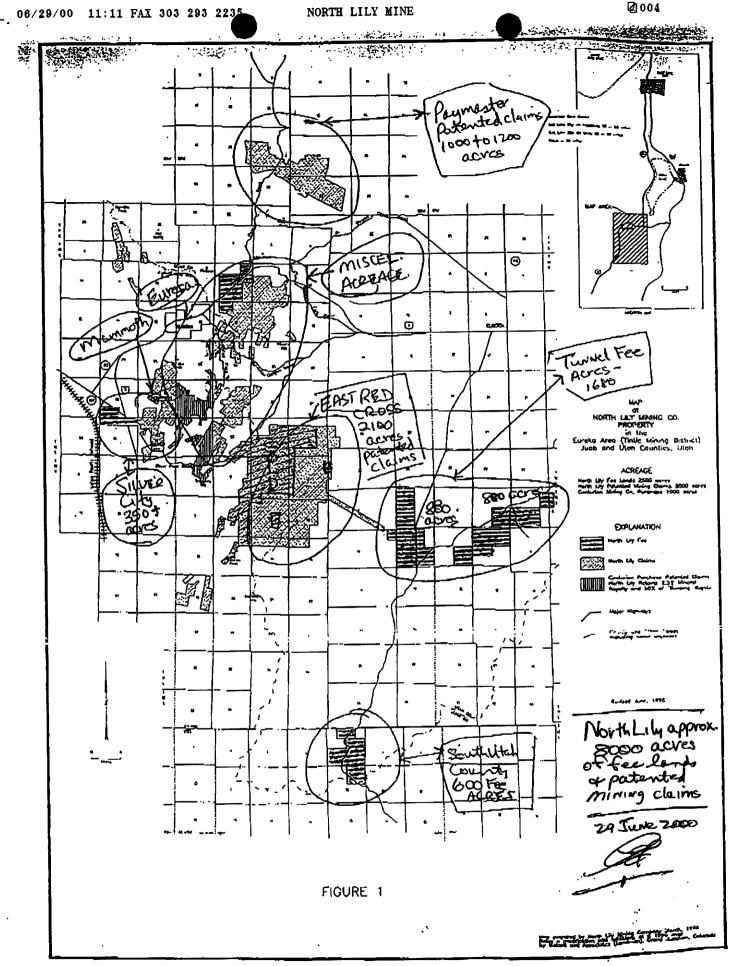

Pages:

NOTES:

ACTUAL ACREAGE Adds up to

890.44 ACRES

PARCEL #A

ACRES

PARCEL #A

ALL PARCEIS Adds up to

#804,000 (PARCEL#A)

Go the 890 are paul A

864 776 160

PAGEZ

ンにたべ

Sharon D. Shirk

100122111004

Master Residential Appraiser, NAMA

P.O. Box 1427 . Provo, UT 84603-1427 . 801.225.4696 voice . 801.225.7652 fax

February 28, 2000

North Lily Mining Company 1800 Glenarm Place, Ste, 210 Denver, CO 80202

Gentlemen:

Appraisals on the following Utah County, UT properties have been shipped to you via Federal Express with delivery on Tuesday, February 29, 2000:

	1	est mkt value
Parcel 1	50.83 acres	\$ 50,500
Parcel 2	50,83 acres	50,500
Parcel 3	50,83 acres	50,500
Parcel 4.	50.83 acres	50,500
	50.83 acres	50,500
Parcel 5	50j.83 acres	50,500
Parcel 6		51,000
Parcel 7	501.83 acres	51,000
Parcel 8	50¦.83 acres	60,000
Parcel 9	60j.25 acres	
Parcel 10	60.24 acres	60,000
Parcel 11	66,84 acres	66,000
Parcel 12	66.84 acres	66,000
Parcel 13	76 ₁₋ 96 acres	69,000
Parcel 14	76: 96 acres	69,000 PARCELA
	75.71 acres .	69,000 \$864,000
Parcel 15	17:17 00000	1 4 60 1 mm 01

Farcels 1-2-3-4-5-6 are located in Section 1. T11S. R2W, Utah County, Utah. Parcels 8-9-10-11-12-13-14-15 are located in Section 12. T11S, R2W, Utah County Utah. Parcels 8-9-10-11-12-13-14-15 are located in Section 12. T11S, R2W, Utah County Utah.

You have advised that you may survey (into 50+acres parcels) your vacant Utah County, Utah land located in Sections 4-5-7-8, Tils, R1W, containing 800 acres in close proximity to the parcels listed above. In such event, it would appear that the vacant land in these sections would have similar value. However, this is not an appraisal.

PARCEL B \$776,000

Very truly yours

Sharon D. Shirk, MRA

PA653

