

0035

*R Incoming  
c/015/0015*

**From:** "Hardy, Russell" <RussellHardy@consolenergy.com>  
**To:** "Hardy, Russell" <RussellHardy@consolenergy.com>, <ogmcoal@utah.gov>  
**CC:** <SteveChristensen@utah.gov>, <karlhouskeeper@utah.gov>, <waynewestern@ut...>  
**Date:** 5/21/2008 6:47 AM  
**Subject:** Emery Subsidence report  
**Attachments:** Emery Subsidence 4-2008.pdf

Attached please find the monthly subsidence report for the Emery Mine.

Thank You,  
-Russell



Russell Hardy  
CONSOL ENERGY  
Phone: (435) 286-3513  
Fax: (435) 286-3516  
email: russellhardy@consolenergy.com


----- "This communication, including any attachments, may contain confidential and privileged information that is subject to the CONSOL Energy Inc.'s Business Information Protection Policy. The information is intended solely for the use of the intended recipient(s). If you are not an intended recipient, you are prohibited from any use, distribution, or copying of this communication. If you have received this communication in error, please immediately notify the sender and then delete this communication in its entirety from your system."

## Consolidation Coal Emery Mine Subsidence Report for April 2008

- 4-25-08 Panel 14 and 15 West – No change observed. BH  
8 South – No change observed. BH  
0 North – No change observed. BH
- 5-8-08 Panel 14 West – No change observed. BH  
Panel 15 West – Two small cracks developing. BH  
8 South – No change observed. BH  
0 North – No change observed. BH
- 5-12-08 8 South – No change observed. BH  
0 North – No change observed. BH  
Panel 15 West - No change observed. BH  
Road and Power – Cracks under powerline appear larger. BH  
Panel 14 West – The landowner contacted the company and let the company know he had found a large crack while preparing his field. Company personnel documented the hole on May 12, 2008. Hole measures 10.3 ft long x 5.0 ft wide x 2.0 feet deep and is near the back of the panel. Pictures shown below. The crack was surveyed 5-20-08 and is labeled on the map with that date. BH



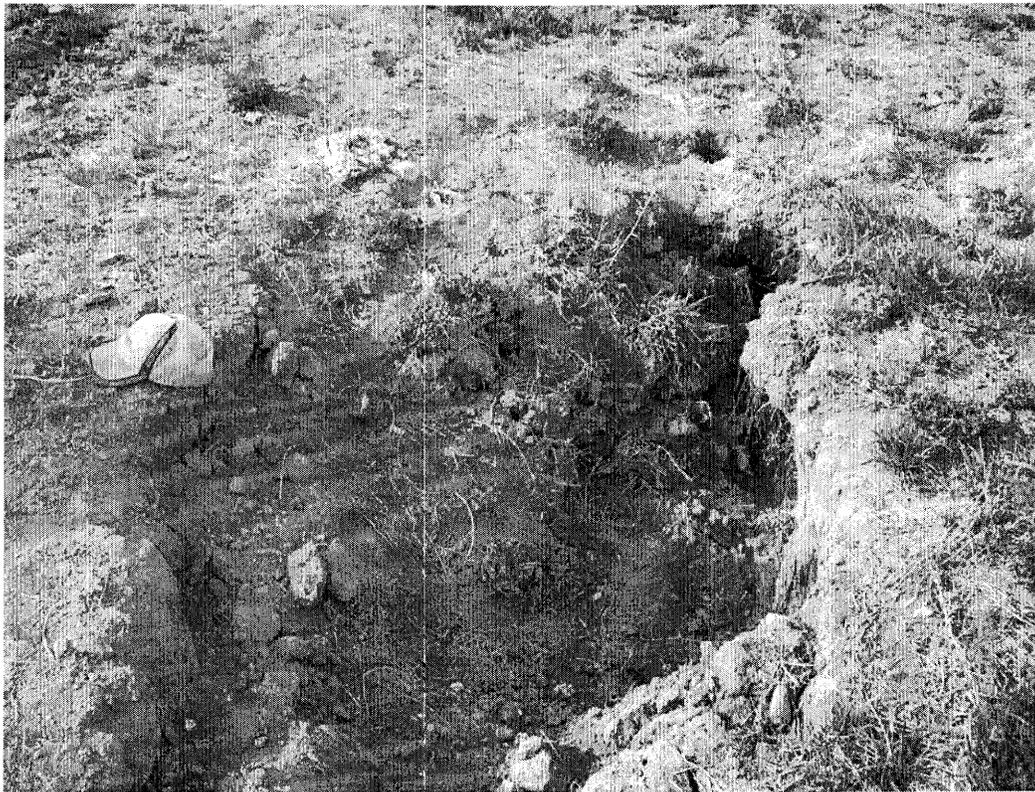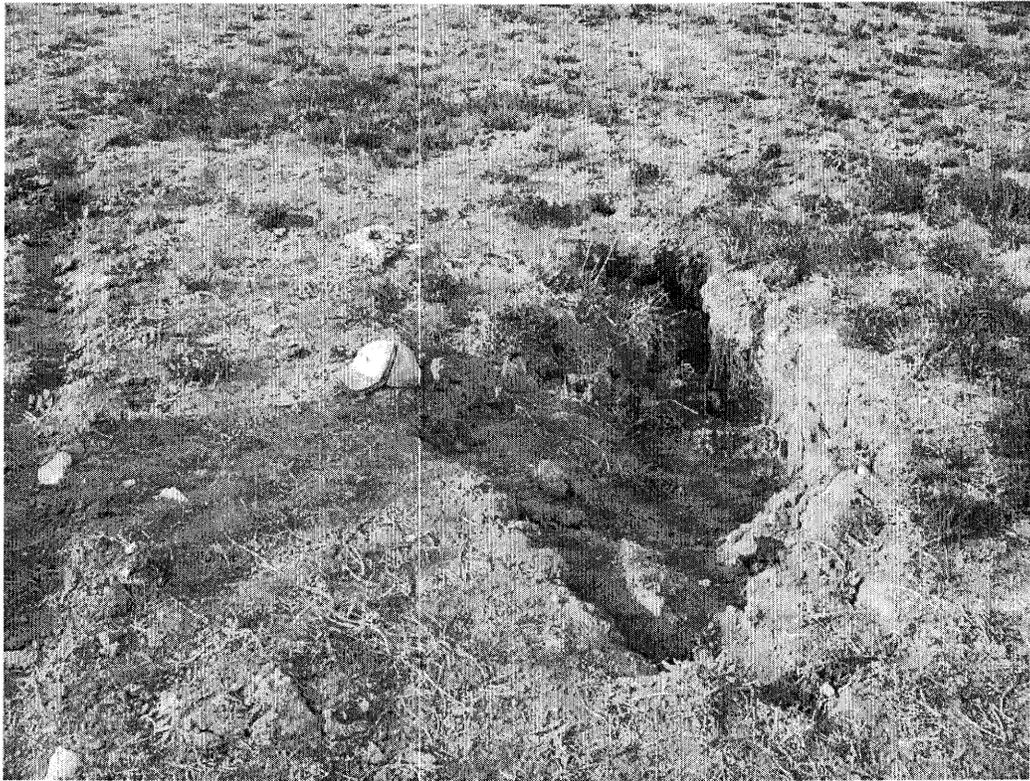

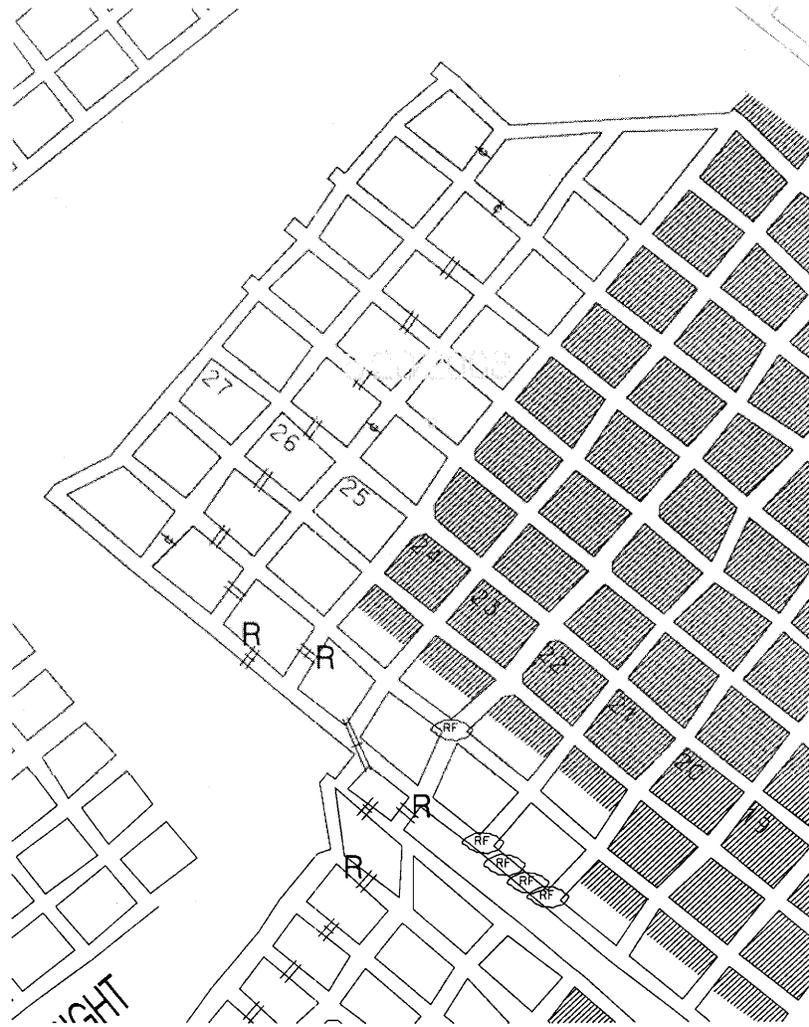

Pillar extraction completed in 8 South on 5-13-08. Both miner units are currently in development and the next retreat location will be Panel 6 West. -RH

Below is a summary of the flow data from SP-10 collected by Karla Knoop, from JBR Environmental.

Consol Emery Mine  
Panel 14th West  
Bryant No. 1  
Flow Measurements made at dam  
breach  
Measurements taken by Karla Knoop

Date	Flow (gpm)
6/13/2007	77
7/24/2007	52
8/28/2007	75
9/20/2007	69
10/19/2007	59
11/15/2007	54
12/17/07	frozen
1/15/08	Flowing under, over & through ice/snow; can't measure, but flow appears to be similar to the November flow rate.
2/26/08	67
3/21/2008	90
4/24/08	35
