



# State of Utah

## DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER  
Executive Director

### Division of Oil, Gas and Mining

JOHN R. BAZA  
Division Director

# Inspection Report

Permit Number:	C0150019
Inspection Type:	PARTIAL
Inspection Date:	Friday, April 24, 2015
Start Date/Time:	4/24/2015 11:00:00 AM
End Date/Time:	4/24/2015 12:30:00 PM
Last Inspection:	Thursday, March 26, 2015

Representatives Present During the Inspection:	
OGM	Lisa Reinhart
Company	Kerry Larsen

Inspector: Lisa Reinhart

Weather: cloudy 60's

InspectionID Report Number: 4179

Accepted by: DHADDOCK

5/5/2015

Permitee: **PACIFICORP**  
 Operator: **ENERGY WEST MINING CO**  
 Site: **COTTONWOOD/ WILBERG**  
 Address: **PO BOX 310, HUNTINGTON UT 84528**  
 County: **EMERY**  
 Permit Type: **PERMANENT COAL PROGRAM**  
 Permit Status: **ACTIVE**

#### Current Acreages

4,114.18	<b>Total Permitted</b>
45.32	<b>Total Disturbed</b>
21.29	<b>Phase I</b>
21.29	<b>Phase II</b>
21.29	<b>Phase III</b>

#### Mineral Ownership

- Federal
- State
- County
- Fee
- Other

#### Types of Operations

- Underground
- Surface
- Loadout
- Processing
- Reprocessing

#### Report summary and status for pending enforcement actions, permit conditions, Division Orders, and amendments:

Inspected waste rock site sediment pond to verify cleaning. Inspected main mine site and observed reclamation is proceeding as planned.

# Lisa Reinhart

Digitally signed by Lisa Reinhart  
 DN: cn=Lisa Reinhart, o=DOGM Coal, ou=2410,  
 email=lreinhart@utah.gov, c=US  
 Date: 2015.05.05 14:27:26 -06'00'

Inspector's Signature:

Lisa Reinhart,  
 Inspector ID Number: 69

Date Tuesday, May 05, 2015



**REVIEW OF PERMIT, PERFORMANCE STANDARDS PERMIT CONDITION REQUIREMENTS**

1. Substantiate the elements on this inspection by checking the appropriate performance standard.
  - a. For COMPLETE inspections provide narrative justification for any elements not fully inspected unless element is not appropriate to the site, in which case check Not Applicable.
  - b. For PARTIAL inspections check only the elements evaluated.
2. Document any noncompliance situation by reference the NOV issued at the appropriate performance standard listed below.
3. Reference any narratives written in conjunction with this inspection at the appropriate performance standard listed below.
4. Provide a brief status report for all pending enforcement actions, permit conditions, Divison Orders, and amendments.

	Evaluated	Not Applicable	Comment	Enforcement
1. Permits, Change, Transfer, Renewal, Sale	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
2. Signs and Markers	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
3. Topsoil	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
4.a Hydrologic Balance: Diversions	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
4.b Hydrologic Balance: Sediment Ponds and Impoundments	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
4.c Hydrologic Balance: Other Sediment Control Measures	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
4.d Hydrologic Balance: Water Monitoring	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
4.e Hydrologic Balance: Effluent Limitations	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
5. Explosives	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
6. Disposal of Excess Spoil, Fills, Benches	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
7. Coal Mine Waste, Refuse Piles, Impoundments	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
8. Noncoal Waste	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
9. Protection of Fish, Wildlife and Related Environmental Issues	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
10. Slides and Other Damage	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
11. Contemporaneous Reclamation	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
12. Backfilling And Grading	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
13. Revegetation	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
14. Subsidence Control	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
15. Cessation of Operations	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
16.a Roads: Construction, Maintenance, Surfacing	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
16.b Roads: Drainage Controls	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
17. Other Transportation Facilities	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
18. Support Facilities, Utility Installations	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
19. AVS Check	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
20. Air Quality Permit	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
21. Bonding and Insurance	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
22. Other	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>

**4.b Hydrologic Balance: Sediment Ponds and Impoundments**


The waste rock site sediment pond has been cleaned and was surveyed on 4/21/15. The first quarter inspection report was submitted 4/17/15 and therefore the next quarterly report should contain the inspection and survey information for the cleaned pond (Ref. R645-301-514).

**22. Other**

Substantial reclamation work has been completed and the contractor is still tearing out the concrete of the silo. 2-3' gravel berms have been placed along the gutter as they're going to pull out the guardrail. All buildings from Rhino run have been removed. The contractor is starting to tear out the asphalt in the parking lot. Asphalt is being taken to the landfill. Piles of concrete are piled up to be buried.



# Cottonwood Inspection 04/24/2015

## Main Mine Site

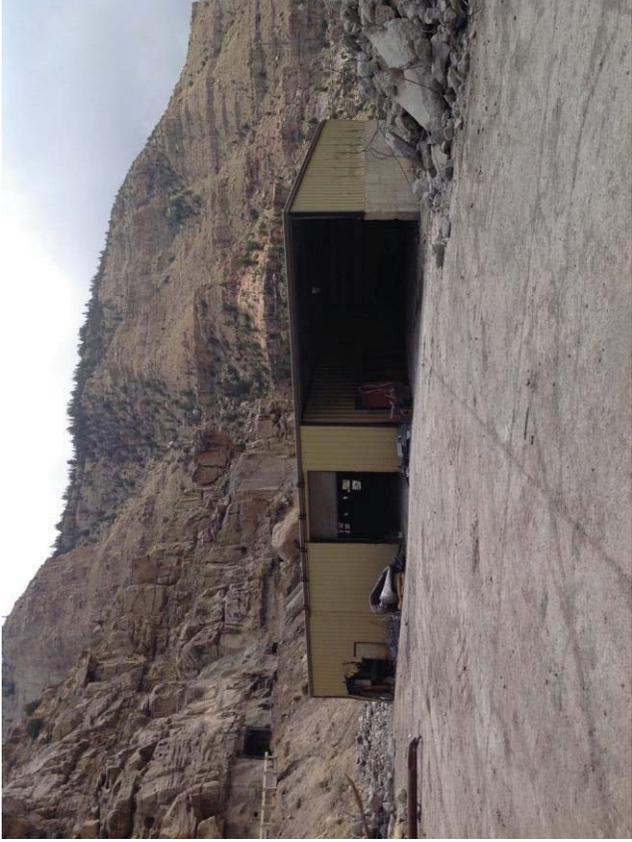

# Cottonwood Inspection 04/24/2015

## Main Mine Site

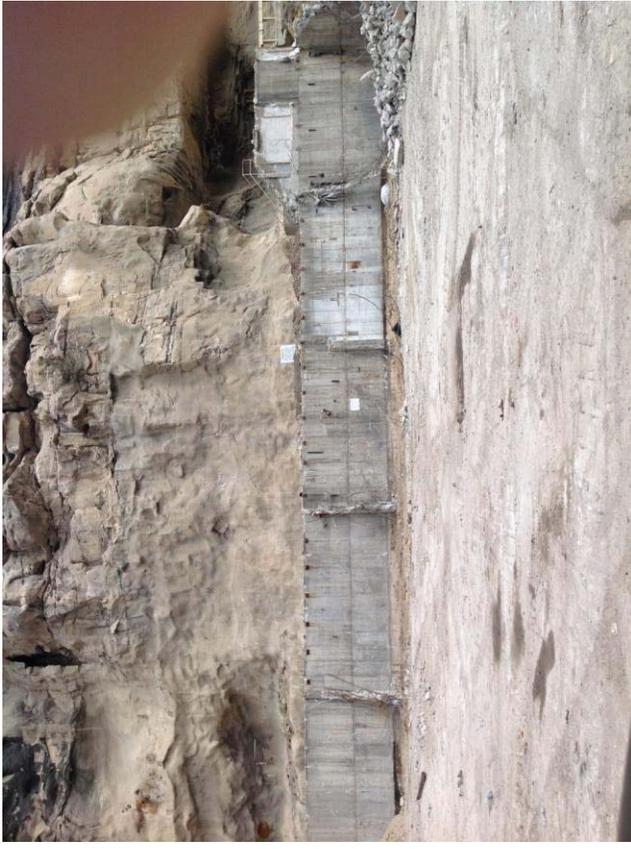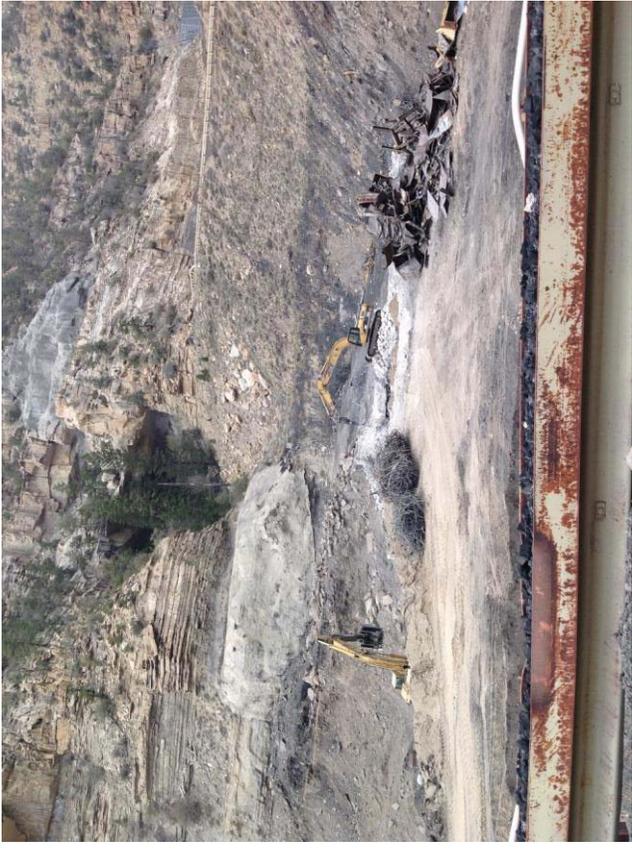

# Cottonwood Inspection 04/24/15 Waste Rock Site

