



State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Inspection Report

Permit Number:	C0250005
Inspection Type:	PARTIAL
Inspection Date:	Wednesday, November 13, 2013
Start Date/Time:	11/13/2013 8:00:00 AM
End Date/Time:	11/13/2013 1:00:00 PM
Last Inspection:	Wednesday, October 16, 2013

Representatives Present During the Inspection:	
Company	Kirk Nicholes
OGM	Karl Houskeeper

Inspector: Karl Houskeeper

Weather: Clear, Temp. 61 Deg. F.

InspectionID Report Number: 3672

Accepted by: jhelfric

11/21/2013

Permittee: **ALTON COAL DEVELOPMENT LLC**
 Operator: **ALTON COAL DEVELOPMENT LLC**
 Site: **COAL HOLLOW**
 Address: **463 North 100 West, Suite 1, CEDAR CITY UT 84720**
 County: **KANE**
 Permit Type: **PERMANENT COAL PROGRAM**
 Permit Status: **ACTIVE**

Current Acreages

635.64	Total Permitted
329.00	Total Disturbed
	Phase I
	Phase II
	Phase III

Mineral Ownership

- Federal
- State
- County
- Fee
- Other

Types of Operations

- Underground
- Surface
- Loadout
- Processing
- Reprocessing

Report summary and status for pending enforcement actions, permit conditions, Division Orders, and amendments:

Fall re-seeding has taken place on a portion of the excess spoil pile.

Mining is being completed in pit #28 and the south side of pit #27 is being opened and material is being placed into the south side of pit #28. Part of pit #28 has been backfilled.

Pit #9 is still open and has not been backfilled, material to backfill this pit is scheduled to come from pit #10.

No additional material has been back filled into pit #6.

Topsoil is still being spread over the top of pit #5.

Karl R. Houskeeper

Inspector's Signature:

Date Thursday, November 14, 2013

Karl Houskeeper,
Inspector ID Number: 49

Note: This inspection report is an official record of compliance with the regulatory program of the Division of Oil, Gas and Mining. telephone (801) 538-5340 • facsimile (801) 359-3940 • TTY (801) 538-7458 • www.ogm.utah.gov



REVIEW OF PERMIT, PERFORMANCE STANDARDS PERMIT CONDITION REQUIREMENTS

1. Substantiate the elements on this inspection by checking the appropriate performance standard.
 - a. For COMPLETE inspections provide narrative justification for any elements not fully inspected unless element is not appropriate to the site, in which case check Not Applicable.
 - b. For PARTIAL inspections check only the elements evaluated.
2. Document any noncompliance situation by reference the NOV issued at the appropriate performance standard listed below.
3. Reference any narratives written in conjunction with this inspection at the appropriate performance standard listed below.
4. Provide a brief status report for all pending enforcement actions, permit conditions, Divison Orders, and amendments.

	Evaluated	Not Applicable	Comment	Enforcement
1. Permits, Change, Transfer, Renewal, Sale	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
2. Signs and Markers	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
3. Topsoil	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
4.a Hydrologic Balance: Diversions	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
4.b Hydrologic Balance: Sediment Ponds and Impoundments	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
4.c Hydrologic Balance: Other Sediment Control Measures	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
4.d Hydrologic Balance: Water Monitoring	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
4.e Hydrologic Balance: Effluent Limitations	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
5. Explosives	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
6. Disposal of Excess Spoil, Fills, Benches	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
7. Coal Mine Waste, Refuse Piles, Impoundments	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
8. Noncoal Waste	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>
9. Protection of Fish, Wildlife and Related Environmental Issues	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
10. Slides and Other Damage	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
11. Contemporaneous Reclamation	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
12. Backfilling And Grading	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
13. Revegetation	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
14. Subsidence Control	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
15. Cessation of Operations	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
16.a Roads: Construction, Maintenance, Surfacing	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
16.b Roads: Drainage Controls	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
17. Other Transportation Facilities	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
18. Support Facilities, Utility Installations	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
19. AVS Check	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
20. Air Quality Permit	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
21. Bonding and Insurance	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>
22. Other	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>

2. Signs and Markers

The mine identification sign is in place and contains all of the required information.

4.a Hydrologic Balance: Diversions

The center line of Robinsons Creek has been staked where mining is completed and backfilling has been done. This will allow for the initial stages of the re-establishment of the Robinson Creek.

4.b Hydrologic Balance: Sediment Ponds and Impoundments

Visited sediment ponds 1, 1B, 2, 3, and 4. Pictures of the ponds was taken and attached to the PDF version of this inspection report.

6. Disposal of Excess Spoil, Fills, Benches


Pictures of the North side of the excess spoil pile was taken and are attached to the PDF version of this inspection report. Additional seeding was done since the last inspection.

8. Noncoal Waste

Several items of noncoal waste was observed along side the access road and access ditch to the office/truck load-out. Arrangements were made to gathered the items prior to the close of the inspection.




Sediment Pond #2

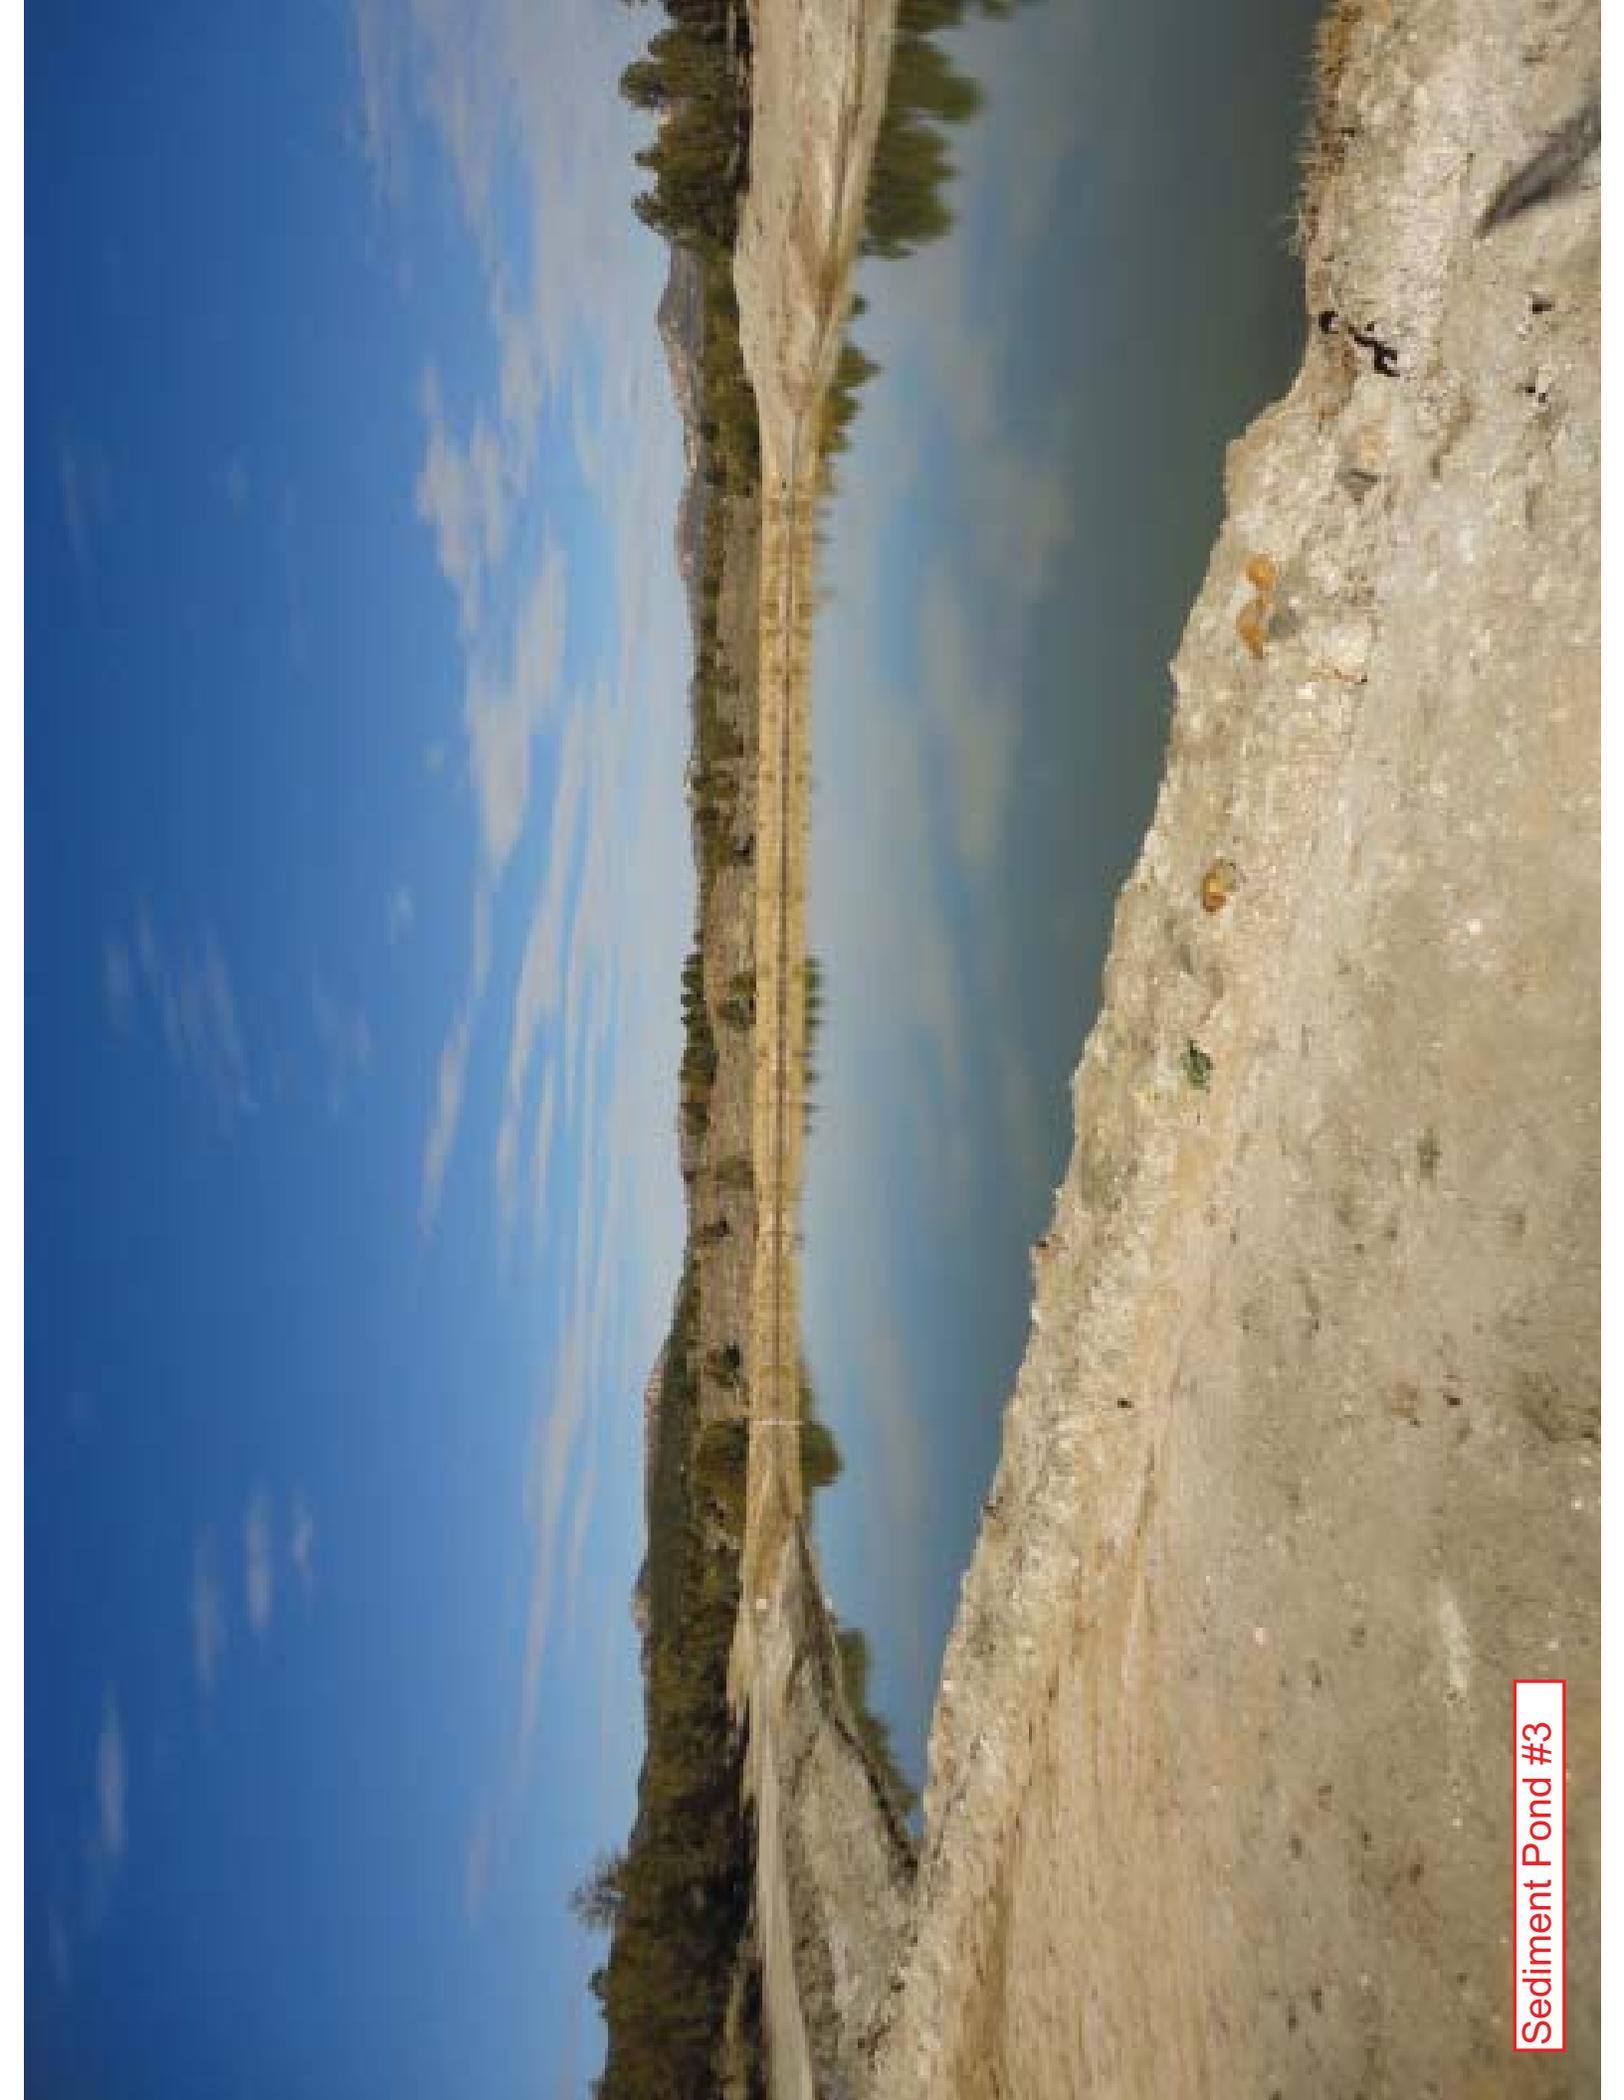

Sediment Pond #3




North Side Excess Spoil Pile

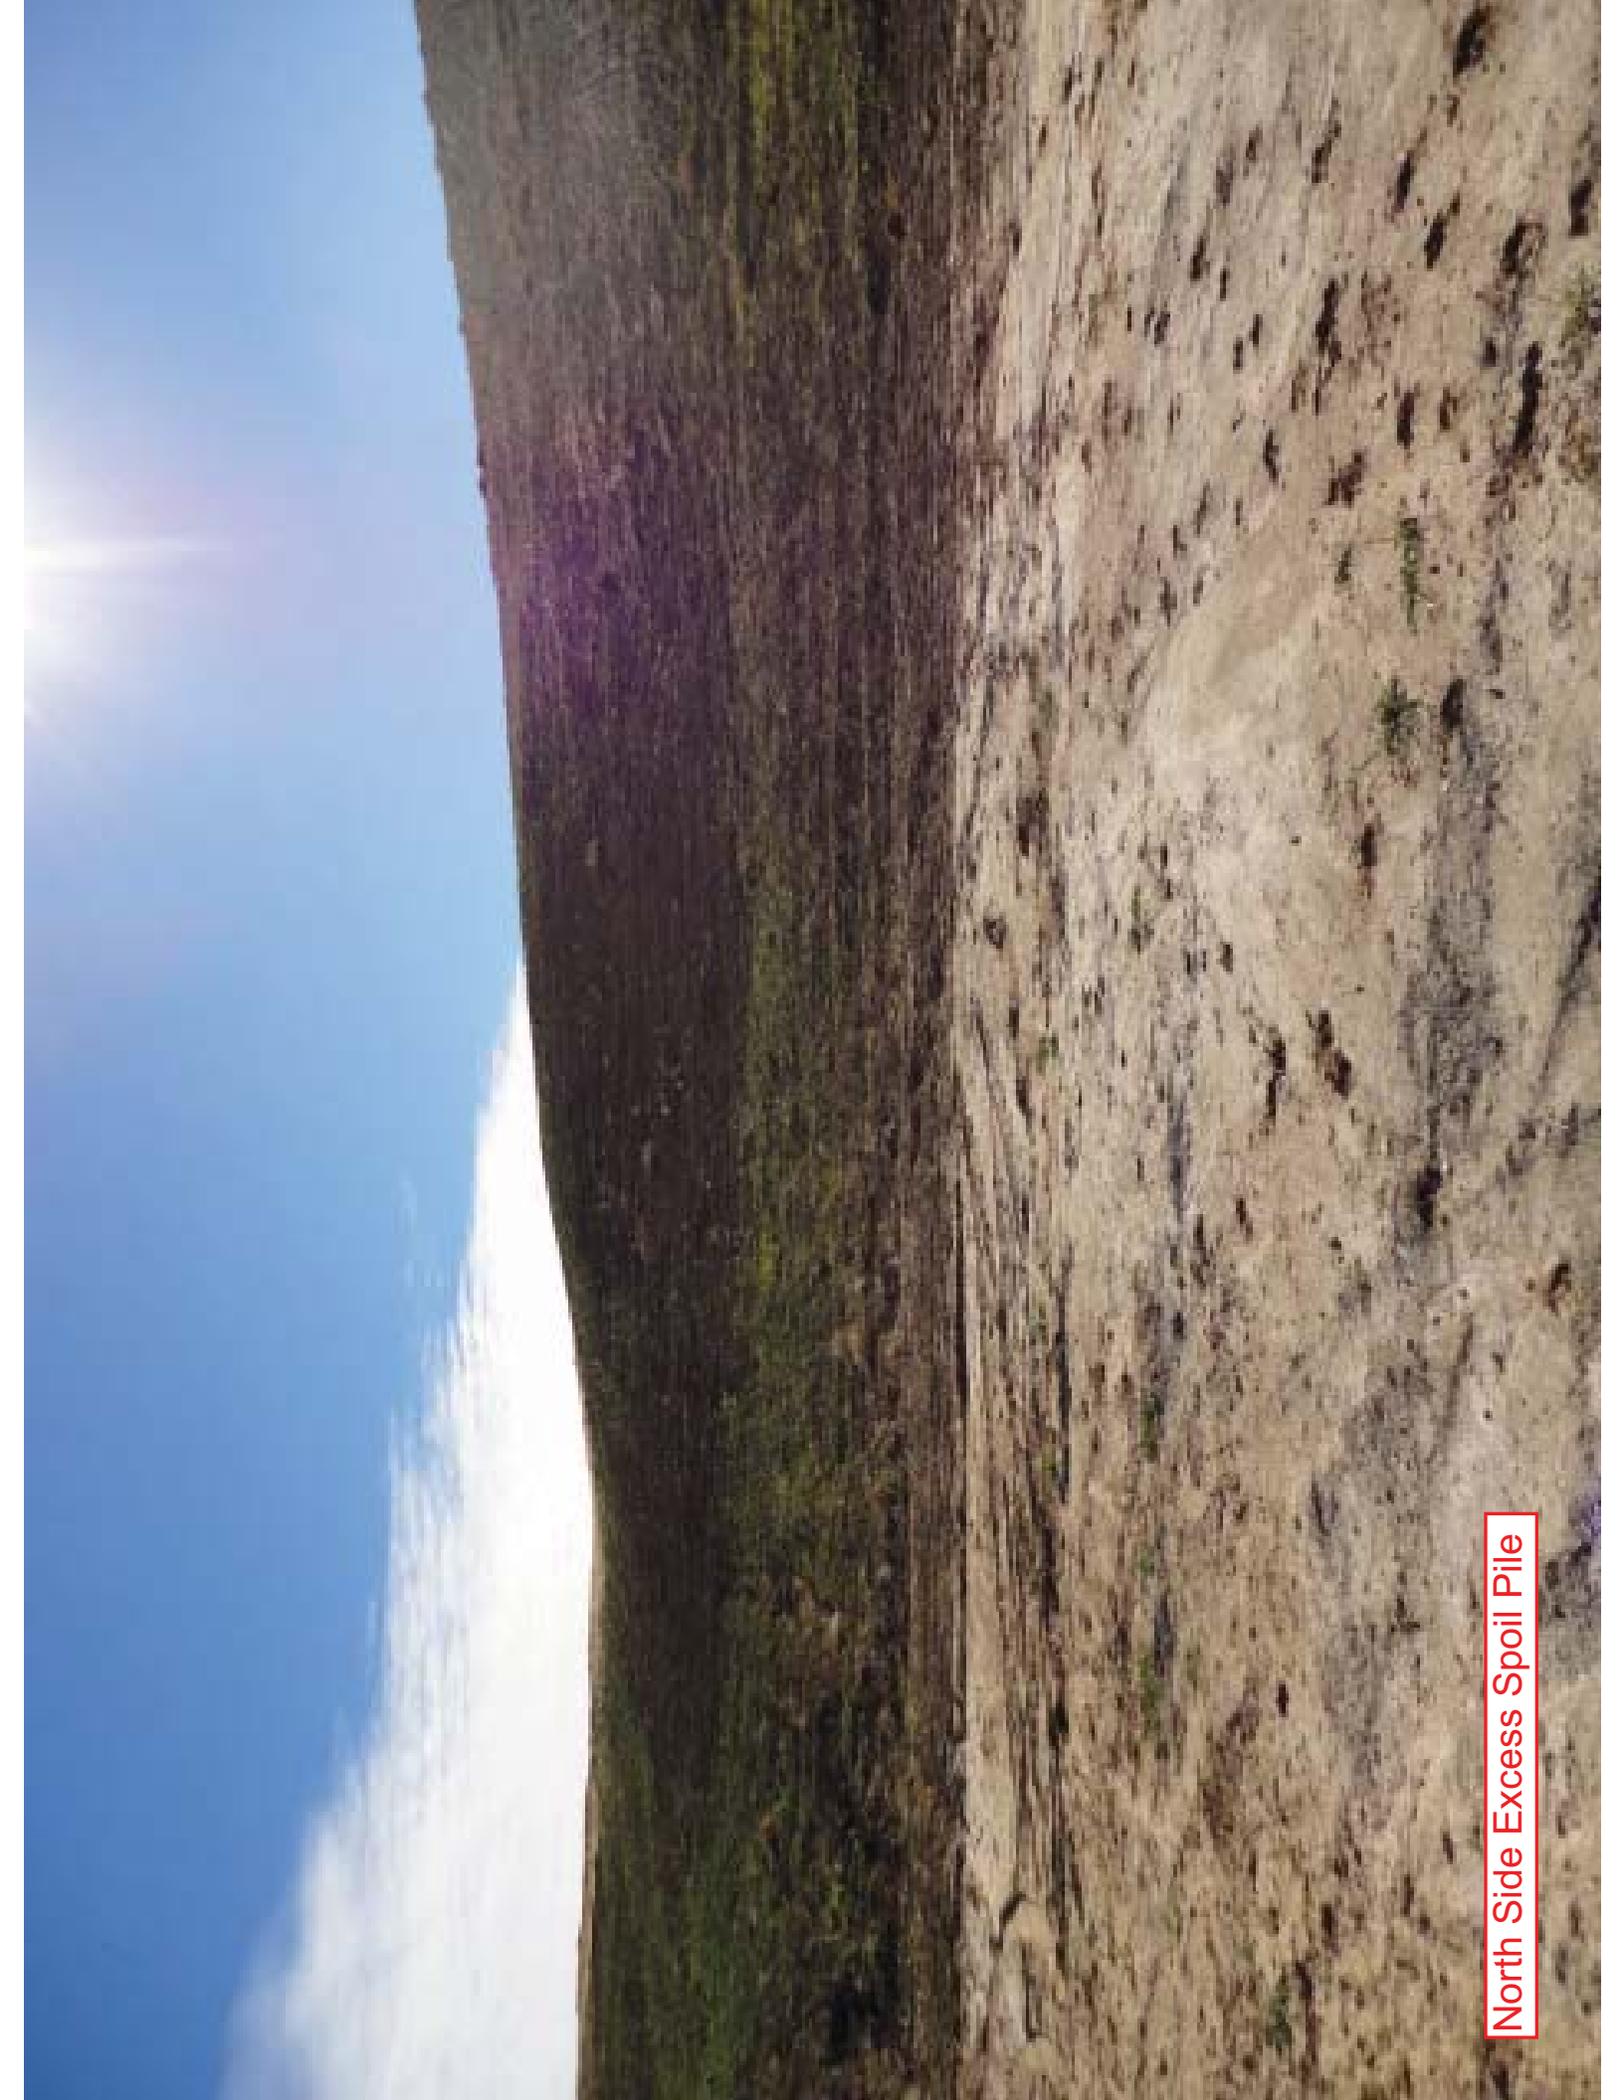


North Side Excess Spoil Pile




North Side Excess Spoil Pile

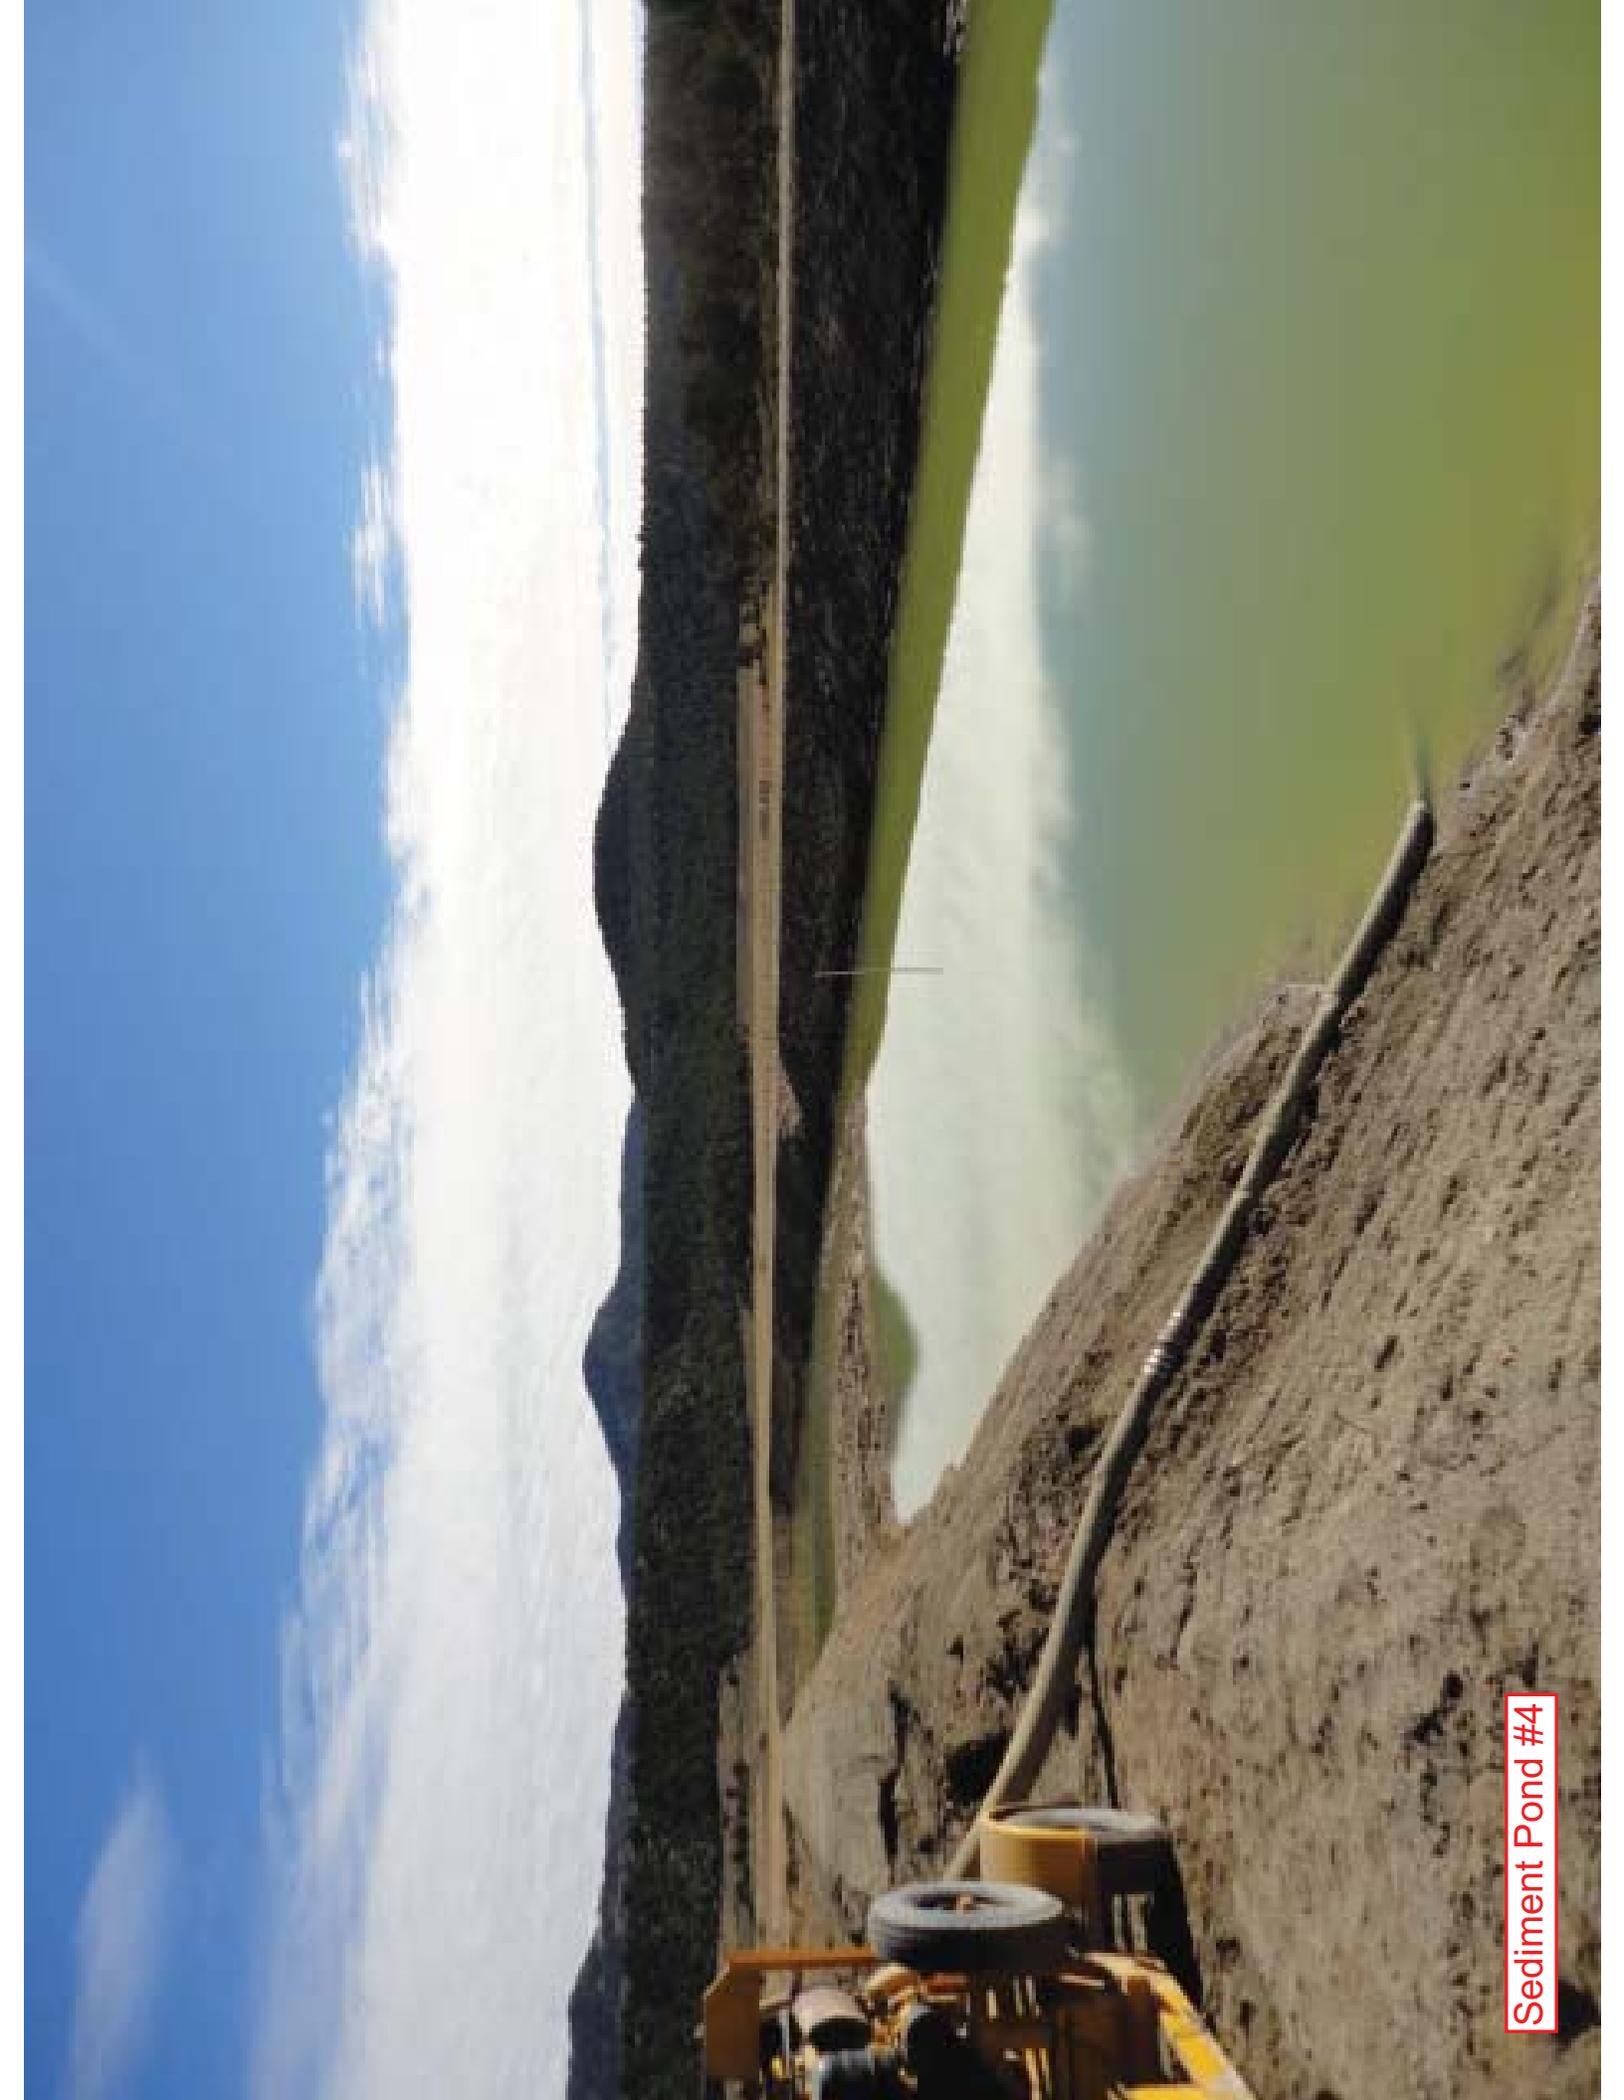


Sediment Pond #4

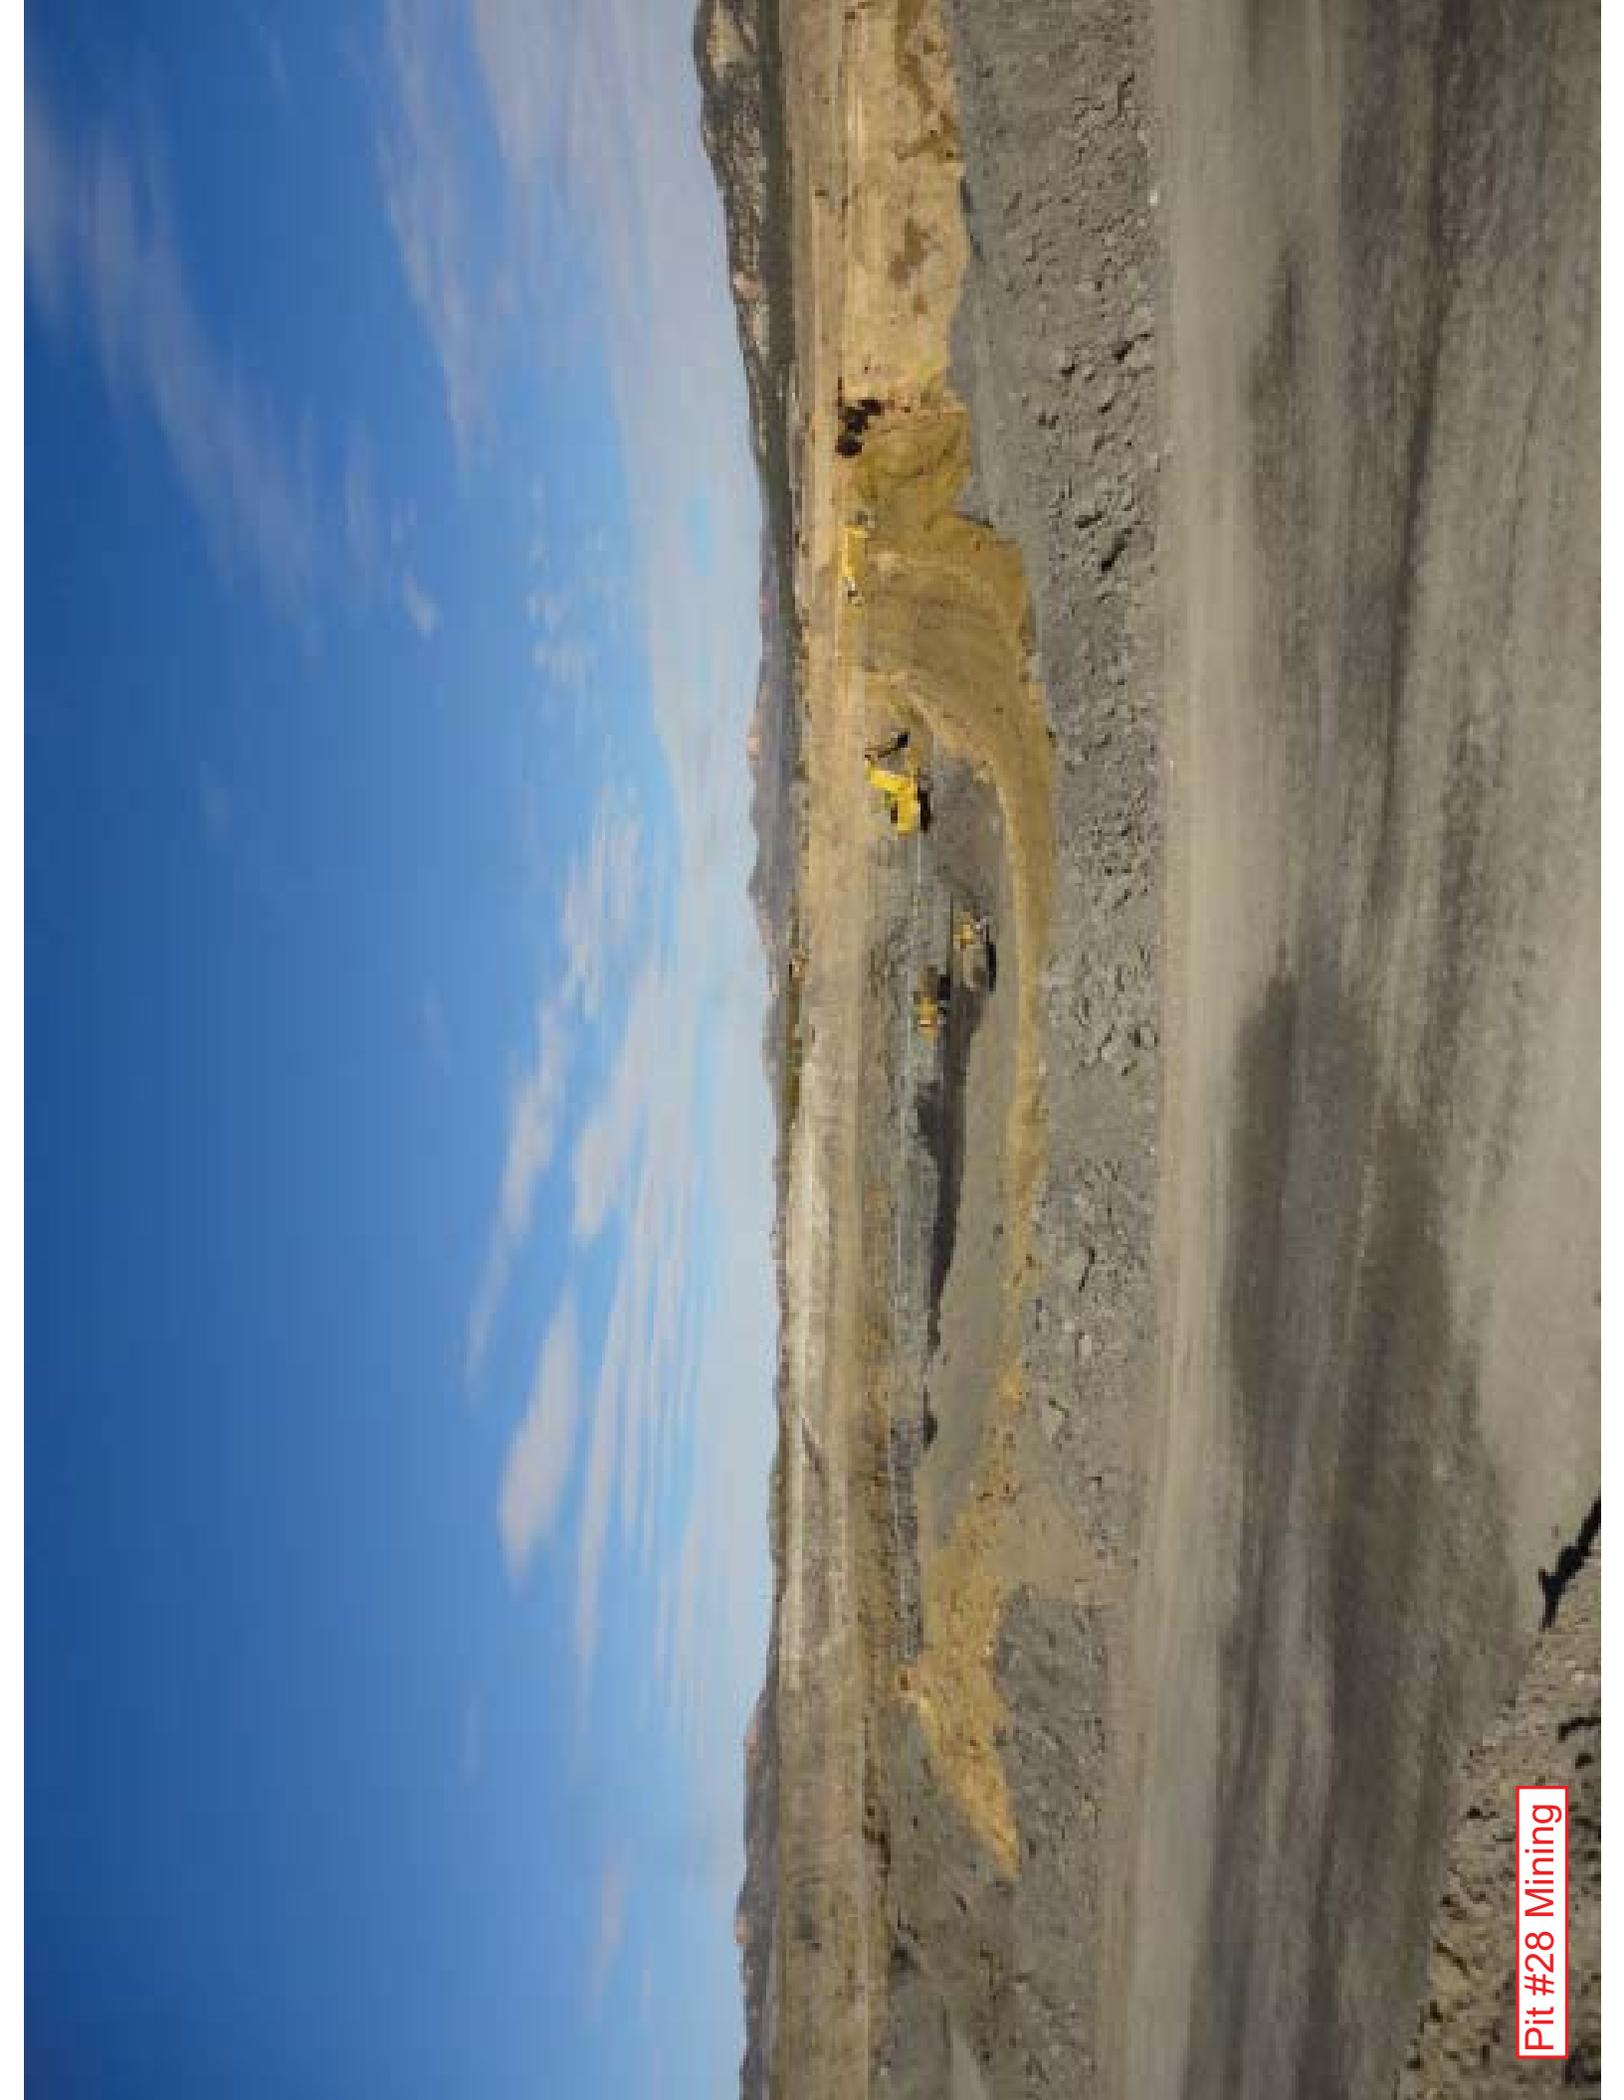

Pit #28 Mining

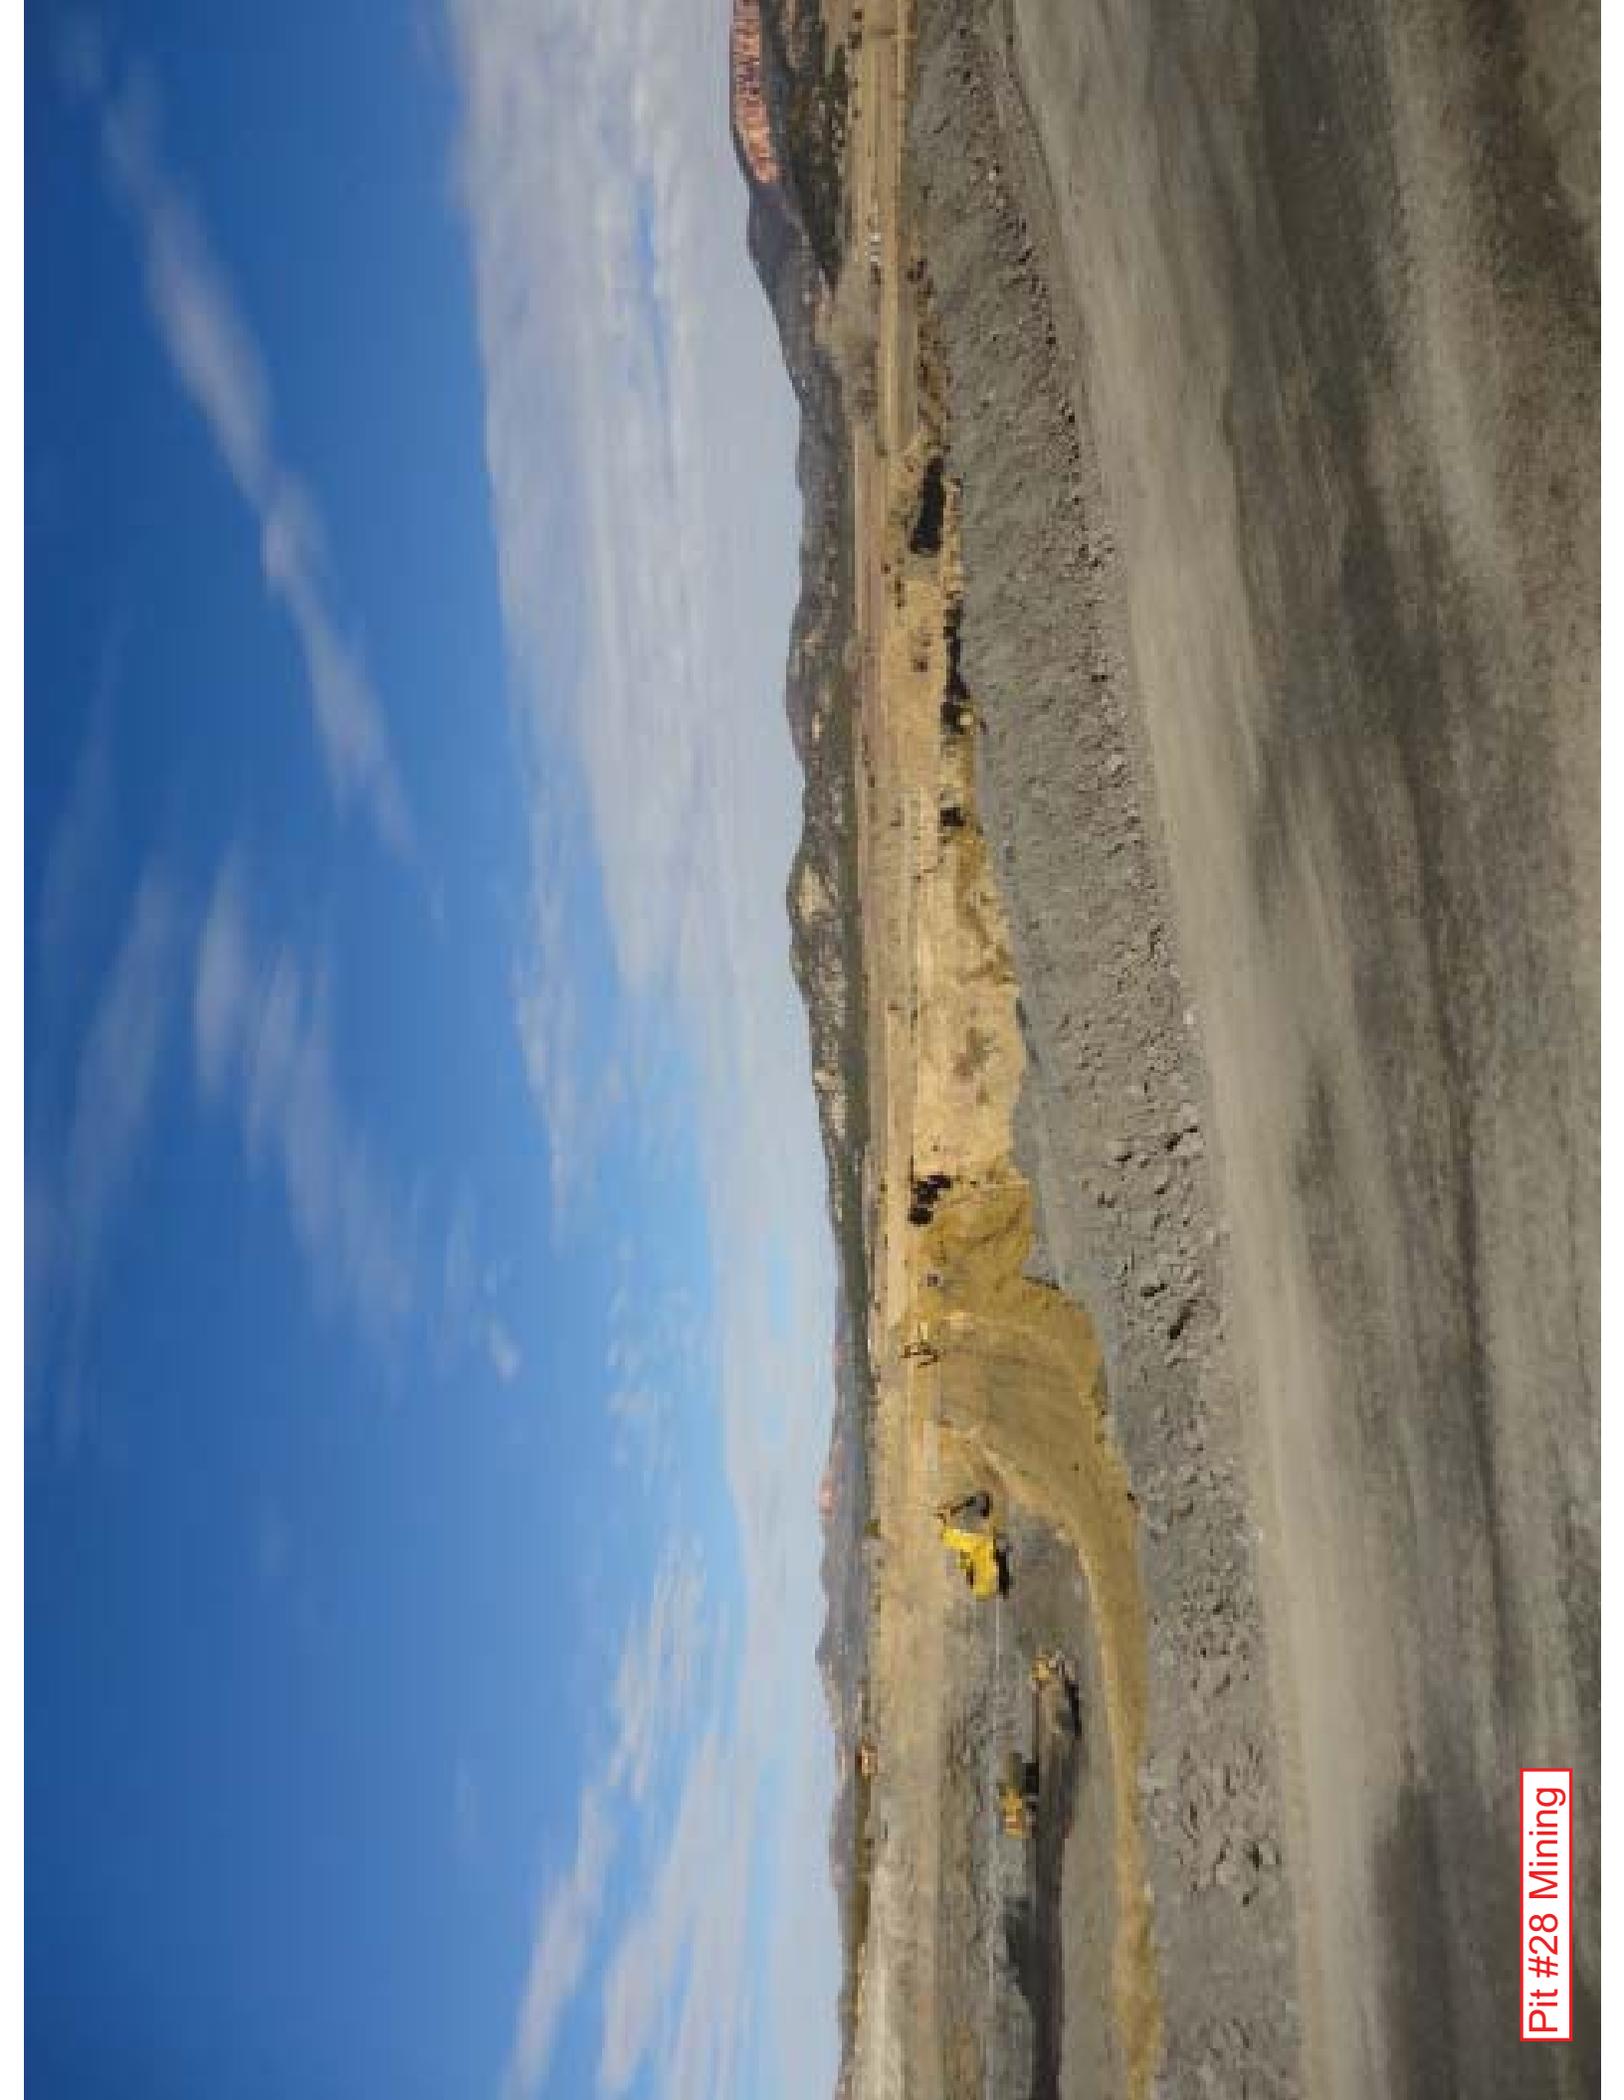

Pit #28 Mining

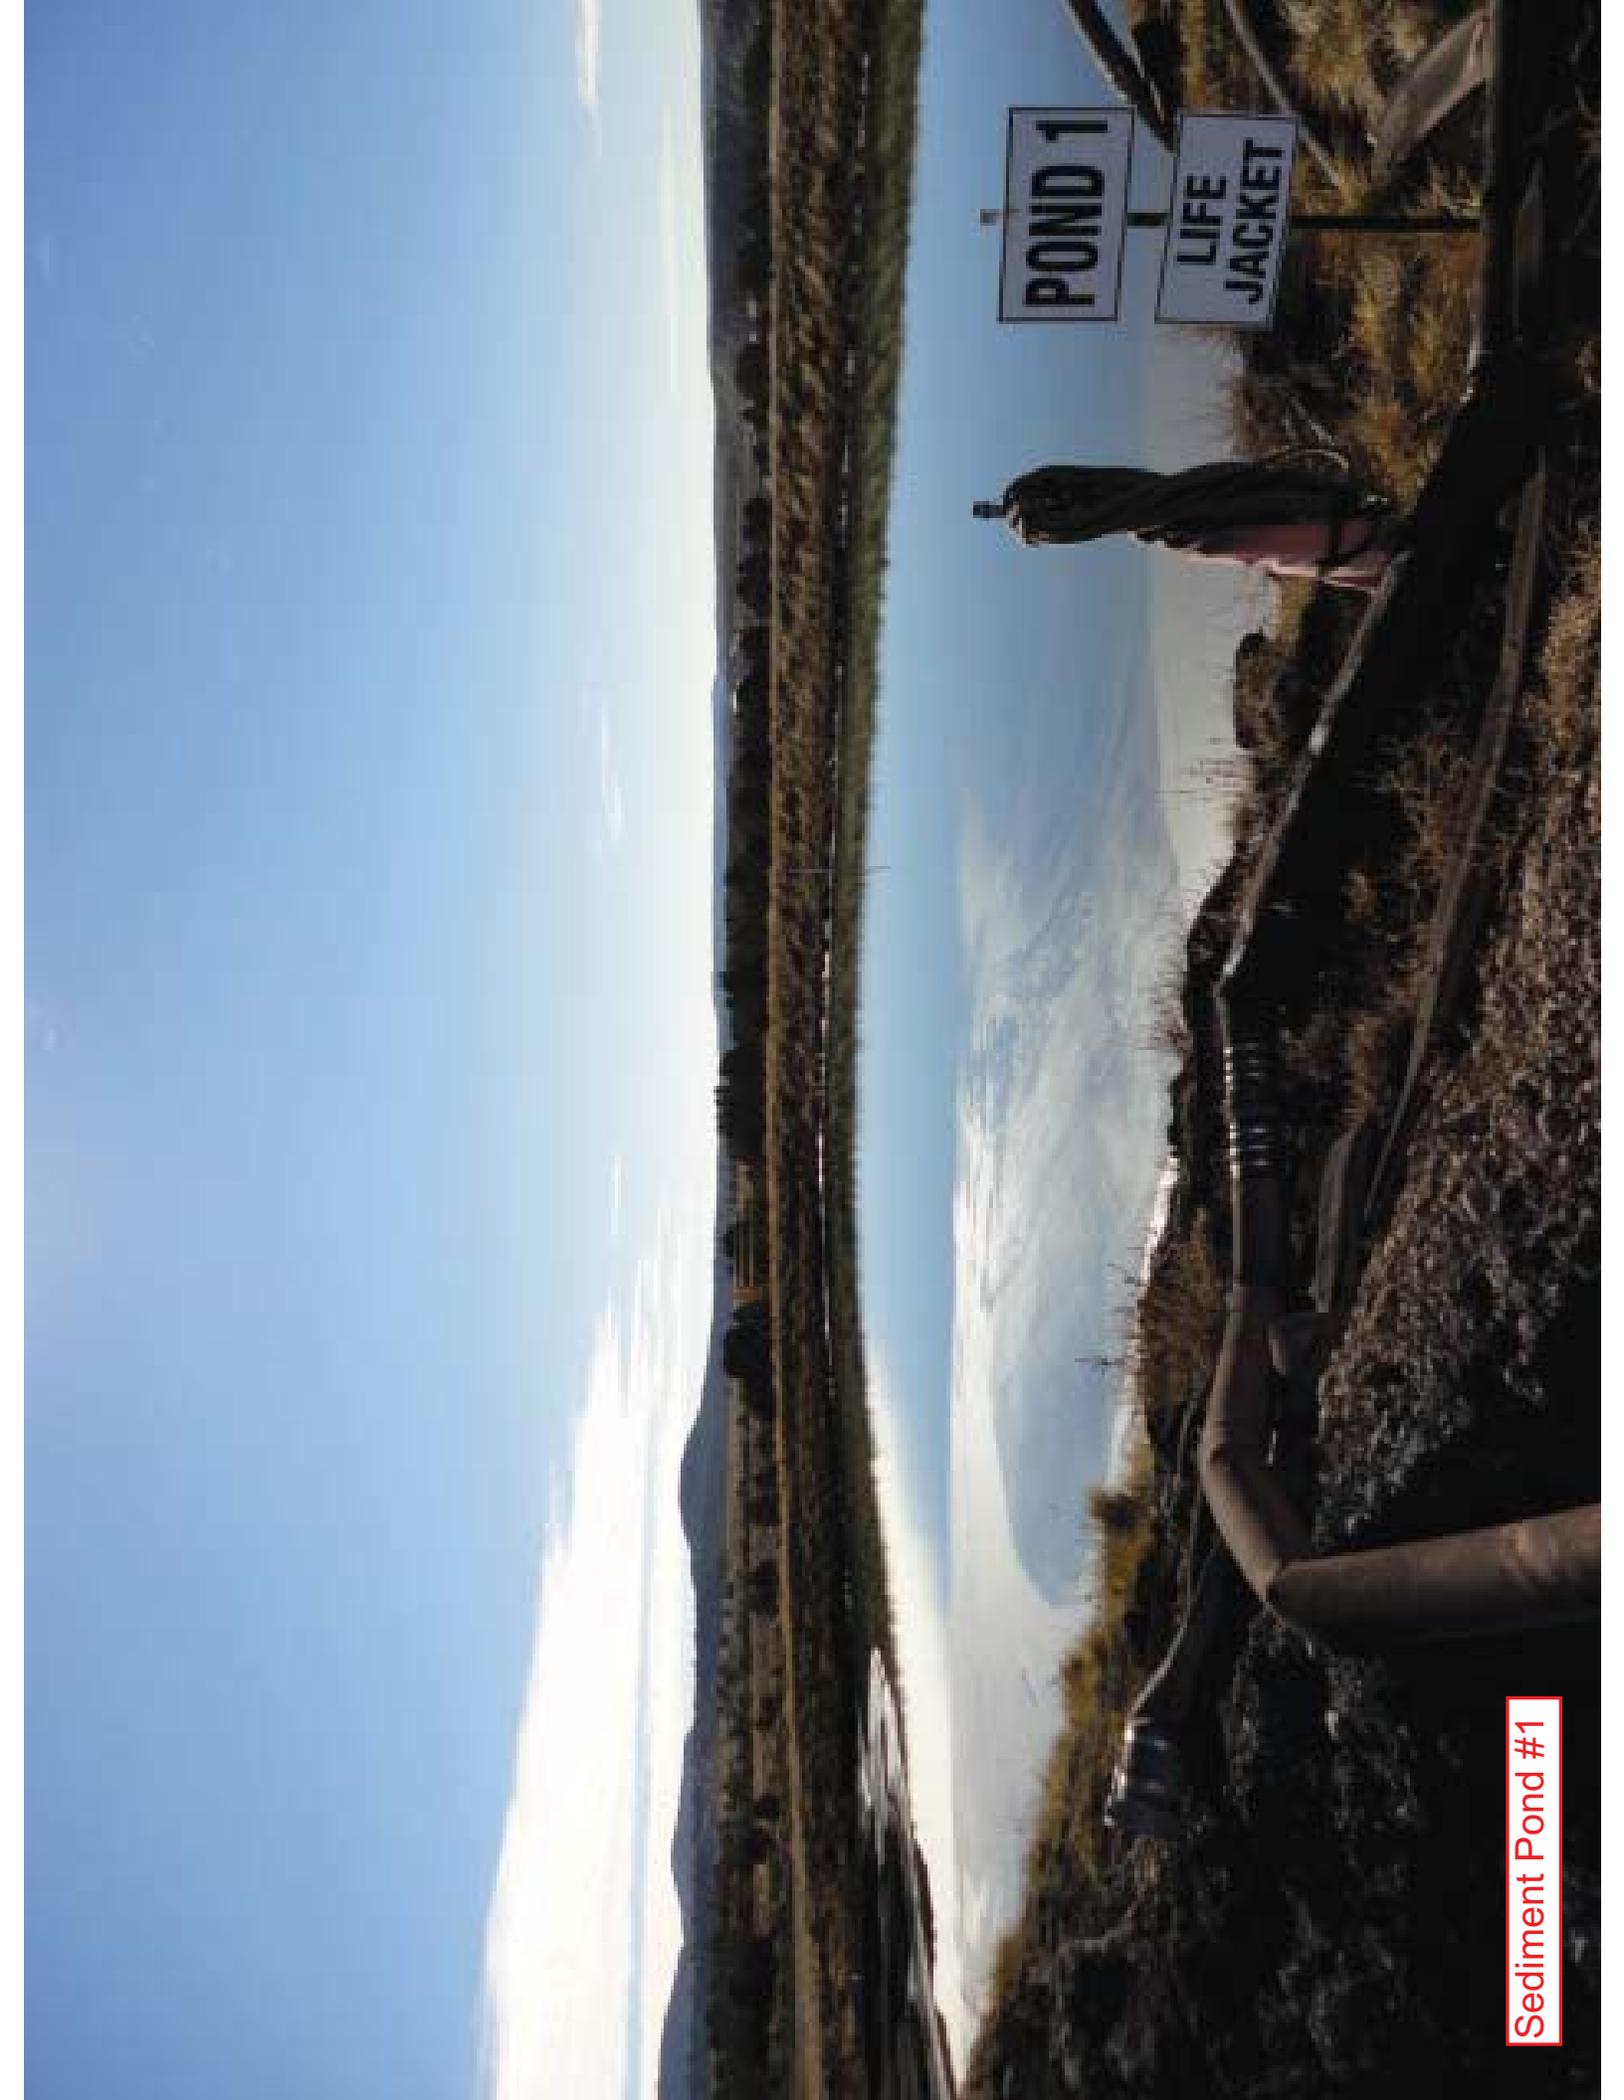

Sediment Pond #1



Sediment Pond #1B
