

GREGORY S. BELL

Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER

Executive Director

Division of Oil, Gas and Mining JOHN R. BAZA

Division Director

Minerals Inspection Report

Reviewed |

PMY

	F	Report Date: 12/08/2014		
Min	e Name: Black Knight	Permit Number: S/01	5/0078 Mine Status:	Active
Operator Name: Goldterra Inc.		Inspection Date: 12/0	B/2014 Permit Fees:	Paid
Inspector(s): Wayne Western		Inspection Time: 10:40 -	11:00 am Bond Amount:	\$7,600
Attendee(s):		Weather:	Bond Escalation:	03/02/2014
Insp	ection Purpose: Routine inspection		Prior Inspection:	10/30/2014
	clusions and Recommendations purpose of this inspection was to determine if the	e site would meet the minimum require	nents for bond release.	
Elements of Inspection		Evaluated & Commented	Enforcement	
1.	Permits, Revisions, Transfer, Bonds			
	The Operator has not formally requested bond bond release.	release but did make known to the Divi	sion the intention to reclaim the s	ite and apply for
2.	Public Safety (shafts, adits, trash, signs, highway	alls)		
	The site was a test pit. No underground openings, highwalls were constructed. No signs or trash were within the permit area.			
3.	Protection of Drainages/Erosion Control			
	The site will be protected from erosion by back pocks for seeds to collect.	filling and grading. The contractor wal	ked tracked machinery over the s	site to create
4.	Deleterious Material			
	None on site			
5.	Roads (maintenance, surfacing, dust control, sa	ıfety)		
	The road to the site from roads used for other p	urposes was reclaimed.		
6.	Reclamation			
7.	Backfilling/Grading (trenches, pits, roads, highwalls, shafts)			
8.	Soils			
	No topsoil was salvaged prior to mining. Operator used what material was available.			
9.	Revegetation			
10.	Other			

Inspector's Signature:

CC:

 $File: \ / nrwogmfs 1/OGM/GROUPS/MINERALS/WP/M015-Emery/S0150078-BlackKnight/inspections/Insp12082014.pdf$




Mine:




Page 3 of 3

Mine: S/015/0078 Inspected: 12/08/2014

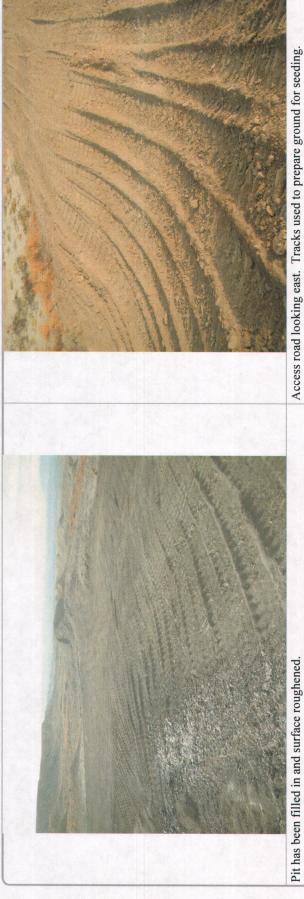



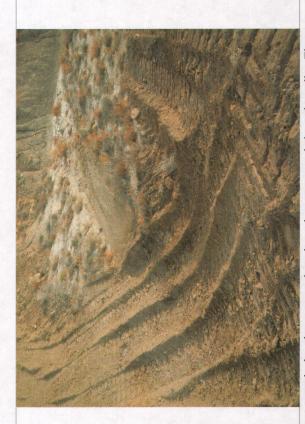

The contractor had to do some earthwork on the access road along the gully. The contractor | Parts of the road were pocked used tracks to create pocks for seeds and moisture to collect.



