



GARY R. HERBERT
Governor
SPENCER J. COX
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Minerals Inspection Report

Report Date: 07/05/2016

Reviewed PPB

Mine Name: Pine Ridge Rock Products	Permit Number: S/057/0010	Mine Status: Suspended
Operator Name: Pine Ridge Excavation and Landscapes	Inspection Date: 06/30/2016	Permit Fees: Paid
Inspector(s): M. Bradley	Inspection Time: 11:45am	Bond Amount: \$68,750
Attendee(s): Iris Hennon and with Weber County Planning	Weather: Cool, rainy	Bond Escalation: 09/30/2019
Inspection Purpose: Follow up from enforcement		Prior Inspection: 11/13/2015

Conclusions and Recommendations

Location: SW1/4 Sec 28 & NW 1/4 Sec 33, T8N, R1E, SLBM. Wanted to inspect for regrading completeness, monitor if more mining was happening, and check revegetation. Gate was locked and could not access the site by vehicle. Weather was not amenable to going in by foot as it was raining and we did not have rain gear available. However, what could be seen is that the water truck is still on site as well as a grizzly for sizing rock. These pieces of equipment need to be removed. There is also a pile of rock remaining on the site, as was agreed to previously. There was evidence of Canadian thistle on the road into the mine, as well as surrounding areas. New signs had been posted on the gate stating that the area was now inside the Bluebell Cooperative Wildlife Management Unit through the Division of Wildlife Resources. Return again soon after coordinating access with Jed Wayment. Recommend continued monitoring when access through the gate can be gained.

Elements of Inspection		Evaluated & Commented	Enforcement
1.	Permits, Revisions, Transfer, Bonds	<input type="checkbox"/>	<input type="checkbox"/>
2.	Public Safety (shafts, adits, trash, signs, highwalls)	<input type="checkbox"/>	<input type="checkbox"/>
3.	Protection of Drainages/Erosion Control	<input type="checkbox"/>	<input type="checkbox"/>
4.	Deleterious Material	<input type="checkbox"/>	<input type="checkbox"/>
5.	Roads (maintenance, surfacing, dust control, safety)	<input type="checkbox"/>	<input type="checkbox"/>
6.	Reclamation	<input checked="" type="checkbox"/>	<input type="checkbox"/>
Checked on reclamation status. Areas regraded, water truck and grizzly on site. Some rock piles remain near front of operation.			
7.	Backfilling/Grading (trenches, pits, roads, highwalls, shafts)	<input checked="" type="checkbox"/>	<input type="checkbox"/>
Backfilling and regrading appear partially complete. Area in Cache County does not appear complete, but was not able to directly access them.			
8.	Soils	<input type="checkbox"/>	<input type="checkbox"/>
9.	Revegetation	<input checked="" type="checkbox"/>	<input type="checkbox"/>
This is the first of three growing seasons needed. Could not tell if vegetation effort was producing any seedlings yet.			
10.	Other	<input type="checkbox"/>	<input type="checkbox"/>

Inspector's Signature: M. Bradley

CC: Iris Hennon, Weber County Planning (ihennon@co.weber.ut.us); Chris Harrild, Cache County Planning (chris.harrild@cachecounty.org); Dan Lockwood, Pine Ridge Excavation and Landscapes (dan@pineridgeutah.com); Jed Wayment, Bluebell CWMU (jwayment@allwest.net)

File: /nrwogmfs1/OGM/GROUPS/MINERALS/WP/M057-Weber/S0570010-PineRidge/inspections/TNSP-06302016.pdf






1) Sign at gated entry (by Iris Hennon)



2) New sign listing site as the Bluebell Cooperative Wildlife Management Unit (CWMU) (Iris Hennon)

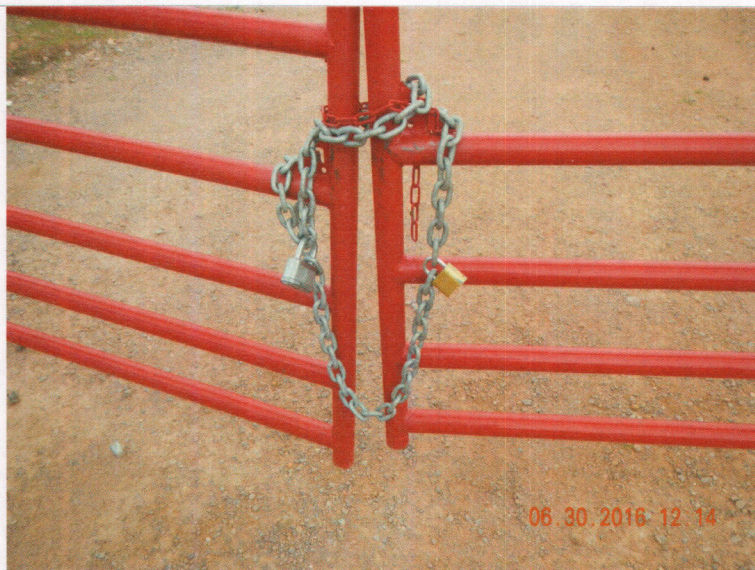


3) Dual-locked gate



4) Safety warning sign on road into site



5) Grizzly and safety station near reggraded main excavation area

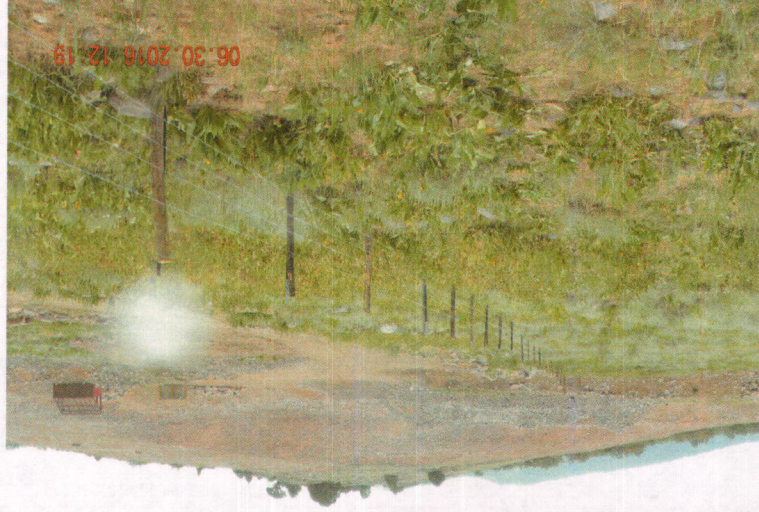

7) Reggraded main excavation area with stockpiled rock to left



6) Water truck still on site



8) Scrap metal still on site



9) Road into site with no fresh tracks



10) Regraded main excavation area with stockpiled rock at right



11) Piled rock near northwest corner of site



12) Canadian thistle on access road going in
