


INF37/003

## F A X T R A N S M I T T A L

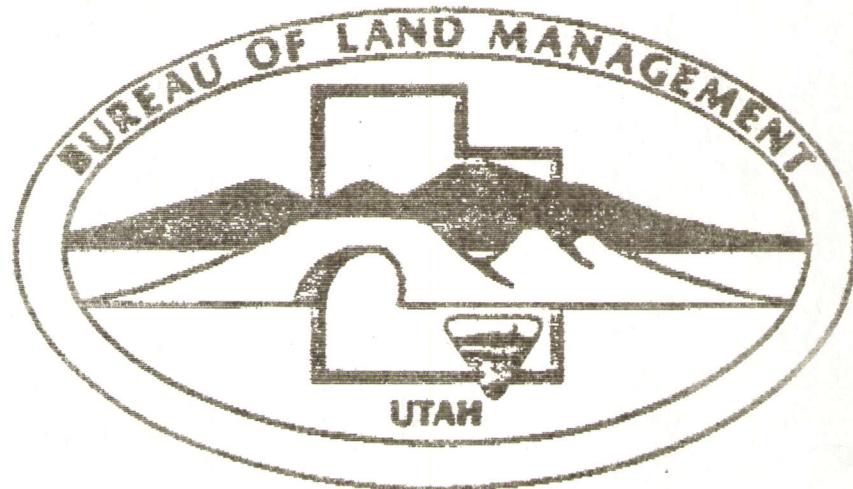

To: HOLLAND SHEPHERD, DOGM  
From: SAC VENTICINQUE, BLW, GRAND RA, UTAH  
Subject: PATTI ANN MINE RECLAMATION  
Number of Pages: Two (2).  
FAX Machine No.: (801) 359-3940  
Date: SEPTEMBER 16, 1991  
Time: 0930 HRS.  
USO Log No.: \_\_\_\_\_  
Comments: Out of the six (6) pages  
FAKED TO ME, THESE TWO ARE RELEVANT  
TO THE PATTI ANN. J.V.

SEP-16-1991 10:33AM FRC

SEP-06-91 16:10 ID:ENERGYFUELS FREDONIA TEL NO:16026437328

TO

88013593940

P.02

#931 P02

9/6/91

SAL -

The Letter Dated 2/8/91 From Holland Shepherd of Doem Resulted from His visit to the Coal, Far West and RABON minesites; During which you were included. Please review Page 2 For Refrence to the coal / RABON concrete Foundations. I Think we are ok with the work completed - If you feel otherwise Please Advise.

Also, For your File, is the PARTI AND Reclamation Plan. - This work will be completed During September 1991 -

This should Be all of the information which you requested. Let me know if you need anything else.

-

Roger Smith

PATTI ANN - M/037/003

Location: Section 33, T29S, R24E

ft 6"

Reclamation Plan:

All structures presently on site will be demolished and rubble buried or removed from the site. If the low grade ore stockpile presently on site exists, the pile will be pushed up against the hillside on the northern side of the existing access road and regraded to a maximum slope gradient of 3H:1V. Topsoil in the immediate vicinity of the pile will be salvaged and used as cover for the pile. If a borrow area for cover topsoil can be established within a two mile radius of the Patti Ann, topsoil adequate to cover the low-grade stockpile with 0.5 feet of soil will be hauled in and spread over the recontoured pile.

The top of the pre-law pad area associated with the Columbus shaft will be ripped and seeded. The waste stockpile located on the Columbus shaft pad will be recontoured and covered with material from the pad. No attempt at reclamation of the spoil pile outslopes will be made, because of their pre-law status.

The existing portal entry will be closed by dozing material into the entry and recontouring the covered portal area. All slopes will be regraded to a maximum gradient of 3H:1V, with the exception of the dump associated with the Columbus shaft.

The entire disturbance area will be seeded with native grass and shrub species recommended by the BLM and UDOGM.

Bond Estimate:

The bond estimate prepared by Frank Filas (UDOGM; 7-27-88) appears to be a good approximation of total liability at the Patti Ann. This estimate is attached.

Total Bond Amount: \$23,800
