File ACT/007/007
& DOE/007/003
Copy to Lee
Route Copy

0008

KAISER STEEL

KAISER STEEL CORPORATION
SUNNYSIDE COAL MINES
SUNNYSIDE, UTAH 84539
TELEPHONE 801-888-4421

RECEIVED
SEP 08 1981
DIVISION OF
OIL, GAS & MINING

3 September 1981

Dept of Natural Resources
Div. of Oil, Gas & Mining
1588 W. North Temple
Salt Lake City, Utah, 84116

JIM
SEP 09 1981

re: Great National Corp.
Crusher Site

Dear Jim,

Great National Corp. is in the process of developing some tar sands in the area using Kendrick Bros. as contractors. They received authorization to proceed from DOGM by letter of 7-16-81 and leased one acre of ground from Kaiser Steel Corp. for a temporary crusher site as shown on the attached drawing. Kendrick Bros agrees to comply with all OSM/DOGM rules and regulations.

Detailed plans are being drawn up showing the crusher facilities, traffic patterns, & surface drainage sediment control structures. This information will be forwarded to your office as soon as it is available. Topsoil will be stockpiled on the south side of the crushee site and protected.

Kaiser Steel Corp. does have ultimate responsibility to assure reclamation compiance, and agrees to assure that all requirements will be complied with.

Sincerely,

John S. Huefner, PE.

John S. Huefner
Reclamation Engineer

Enclosure

cc: Lloyd Heath
Tom Kendrick

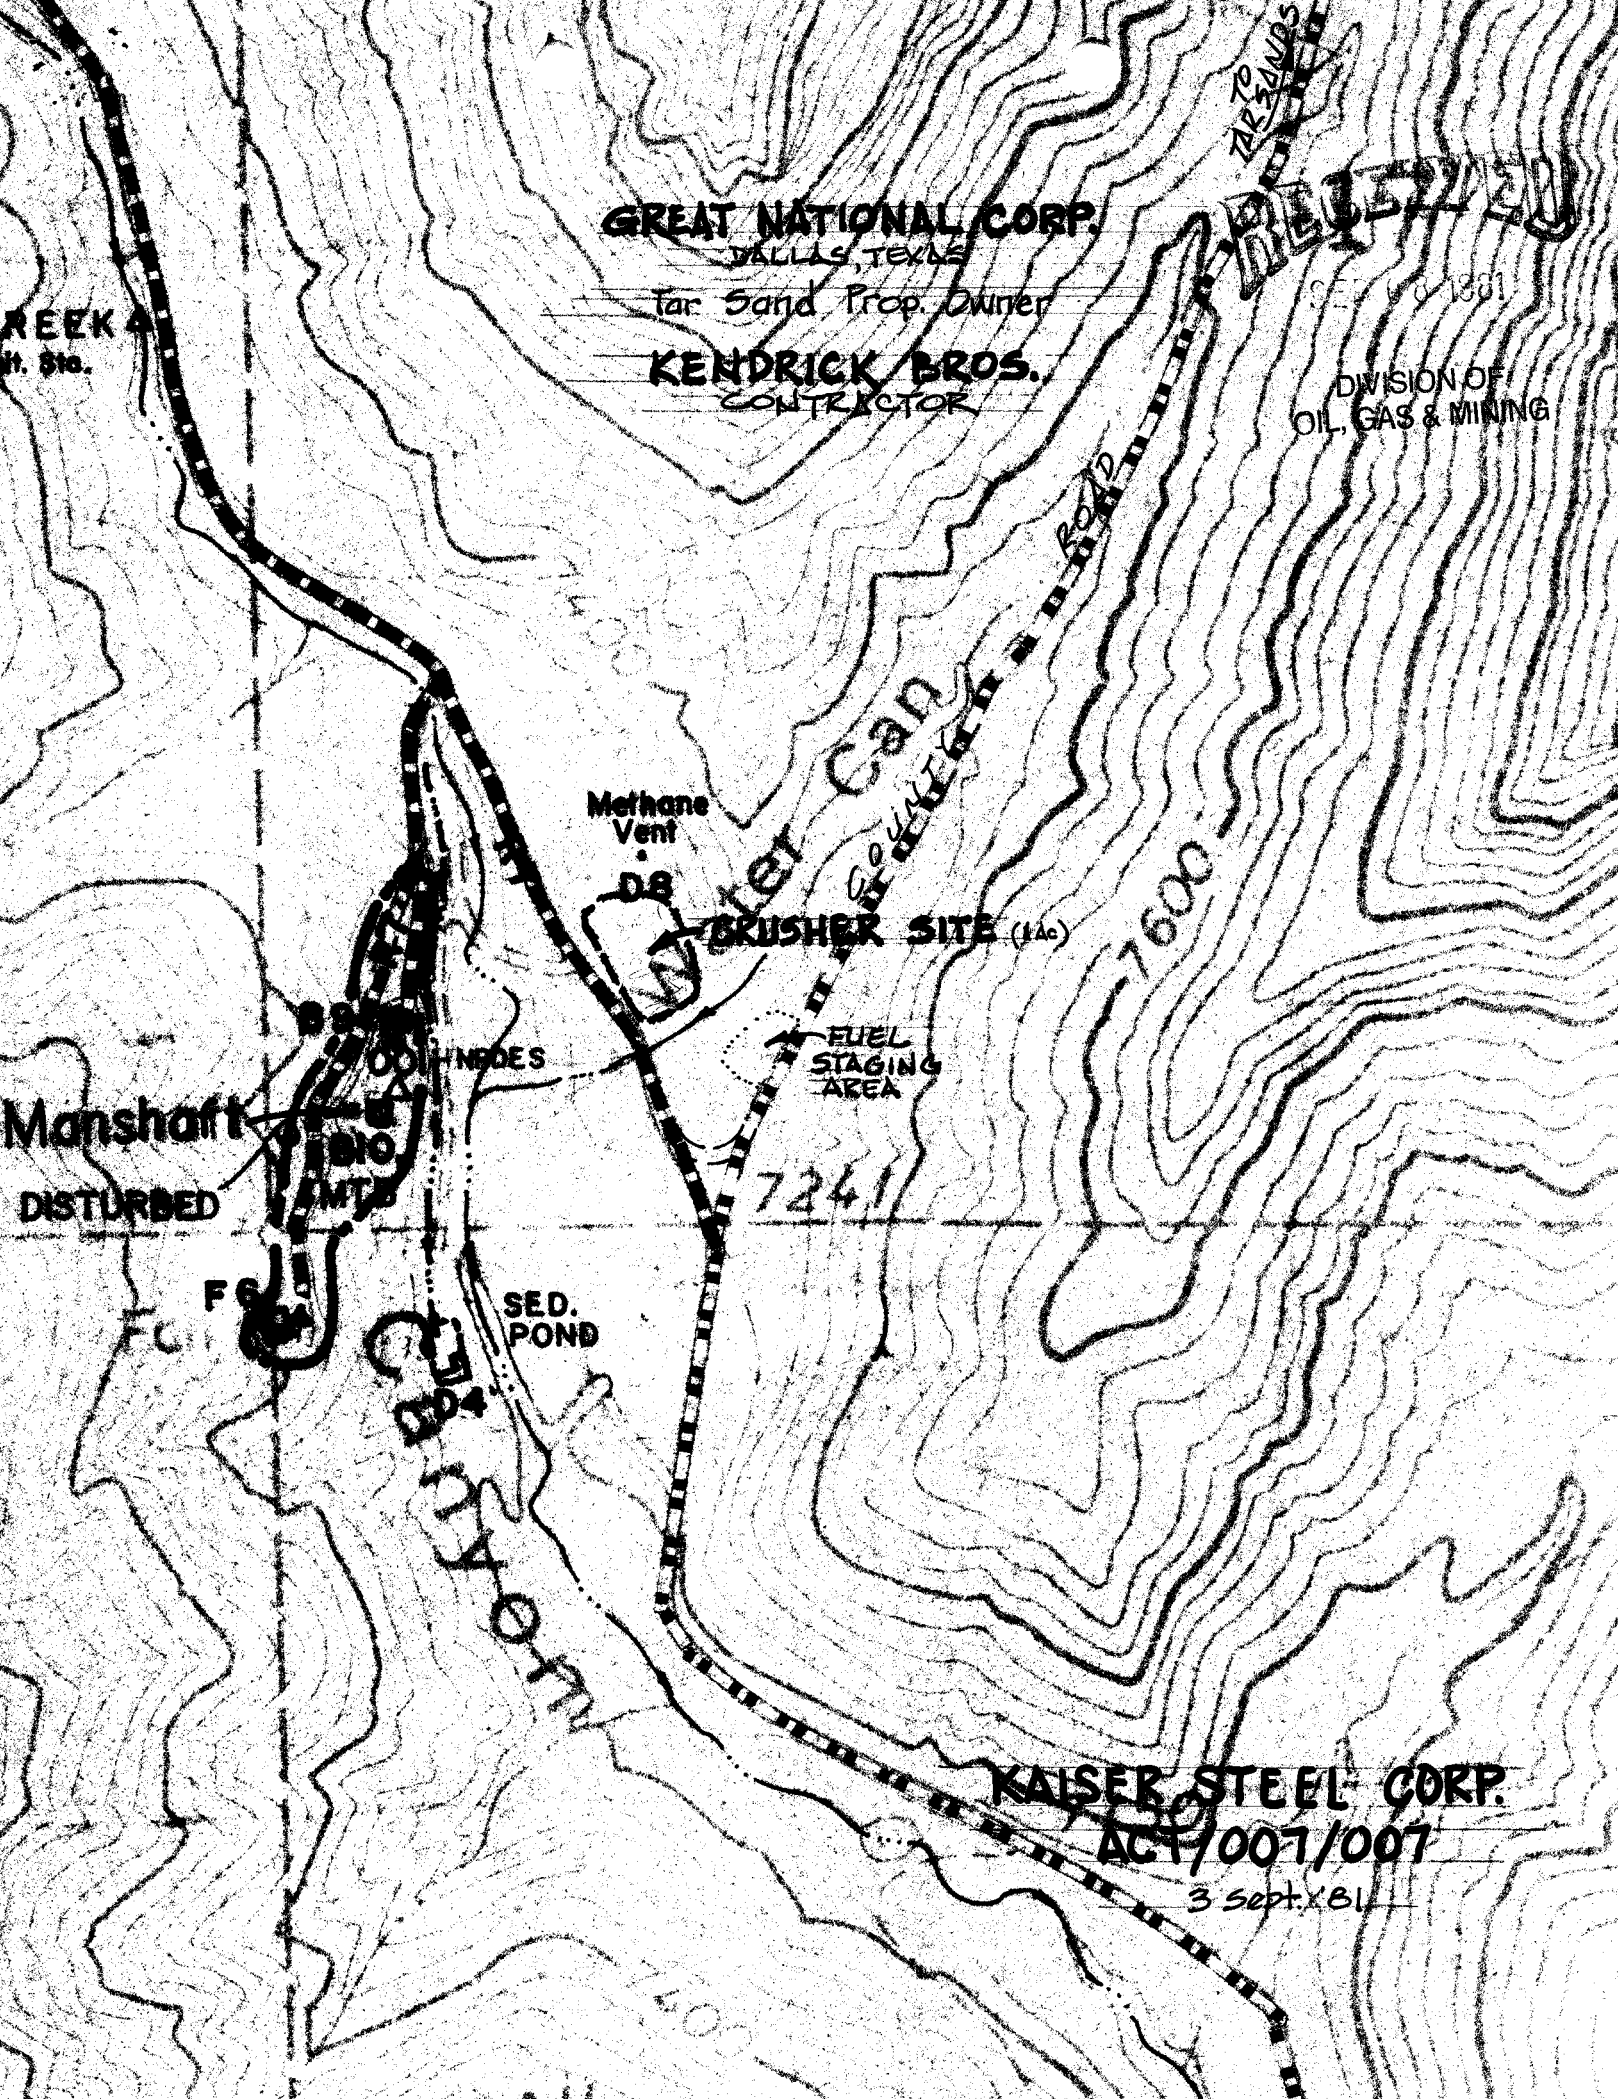
GREAT NATIONAL CORP.
DALLAS, TEXAS
Tar Sand Prop. Owner
KENDRICK BROS.
CONTRACTOR
TO TAR SANDS
DIVISION OF
OIL, GAS & MINING
REEK
Methane
Vent
D8
CRUSHER SITE (1Ac)
FUEL
STAGING
AREA
Water Can
COUNTY
ROAD
7600
7241
Manshaft
DISTURBED
NODES
F6
SED.
POND
D4
KAISER STEEL CORP.
ACT/007/007
3 Sept. '81

STATE OF UTAH
NATURAL RESOURCES & ENERGY
Oil, Gas & Mining

Scott M. Matheson, Governor
Temple A. Reynolds, Executive Director
Cleon B. Feight, Division Director

4241 State Office Building • Salt Lake City, UT 84114 • 801-533-5771

Tom D

December 14, 1981

REGISTERED - RETURN RECEIPT REQUESTED

Mr. John Huefner
Engineer
Kaiser Steel Corporation
P.O. Box D
Sunnyside, Utah 84539

RE: NAOC on Sediment Control Structures
NAOC on Coarse Refuse Roads
Great National Corporation
Crusher and Stockpile Site
Sunnyside Complex
ACT/007/007
Carbon County, Utah

Dear Mr. Huefner:

This letter is intended to document the substance of our recent phone conversation (week of December 7). You may consider this letter as a termination of the NAOC Form dealing with the implementation of straw bale filter dikes near the manshaft and at No. 2 fan. Also, please consider this as official record of the extension until December 18, 1981, of the NAOC Form dealing with erosion and sediment on roads where coarse refuse has been utilized.

Also discussed was compliance work directed at drainage control at the site of the Great National Corporation crusher and stockpile site. Problems were discussed during a December 4, 1981, inspection. As you indicated in your September 1, 1981, letter Kaiser has ultimate responsibility for this site. Hopefully, compliance in this area will be upgraded in the near future and prior to the next inspection. If I may be of any help please don't hesitate to call.

Sincerely,

Thomas L. Portle

THOMAS L. PORTLE
RECLAMATION SOILS SPECIALIST

TLP/te
cc: NOV File
Inspection Staff

Board/Charles R. Henderson, Chairman • John L. Bell • E. Steele McIntyre • Edward T. Beck
Robert R. Norman • Margaret R. Bird • Herm Olsen

an equal opportunity employer • please recycle paper

December 24, 1981

Inspection Memo
to Coal File:

RE: Sunnyside Complex
ACT/007/007
Carbon County, Utah

On December 4, 1981, Division Reclamation Officer Ken Wyatt and Division Reclamation Soils Specialist Tom Portle met with John Huefner who represented Kaiser Steel. The purpose of this inspection was to view areas of concern which had been previously addressed in NAOC forms. The first area viewed was the area near the manshaft where straw bales had been fortified to control runoff from this disturbed area and in order to guard against the possibilty of leakage since oil was stored in this area. However, the straw bales had not been installed properly. Mr. Huefner was informed of deficiencies in this area and committed to taking care of them in the immediate future. The second area looked at was the straw bales associated with the #2 fan in Fan Canyon. Straw bales employed here appeared to be functioning as intended. Reseeding had been done in this area. Reseeding was the topic of other problem areas (see form dated November 6, 1981). All reseeding had been done prior to this inspection and this memo informs Mr. Huefner of termination of this NAOC form.

Another concern brought to light during this inspection was the state of compliance at the Great National Crusher site. Drainage control problems were evident here, the ditch on the road which was to carry water through straw bales and subsequently into a dry drainage was in an ill state of repair. This was brought to Mr. Huefner attention again in the letter mentioned above. This concern as addressed, and this should be inspected on a following inspection to determine if compliance has been achieved.

TLP

THOMAS L. PORTLE
RECLAMATION SOILS SPECIALIST

cc: Tom Ehmett, OSM
John Huefner, Kaiser Steel
Inspection Staff

TLP/btb

Statistics:

Vehicle: EX 68805--487 miles
Per Diem: 2 persons X 1 day, 12.5 hours @ $37.50/day = $53.78
Grant: A & E
