0036

UNITED STATES FUEL COMPANY

P.O. BOX 887
PRICE, UTAH 84501

(801) 637-2252
FAX (801) 343-2344

January 8, 1996

RECEIVED
JAN 18 1996
DIVISION OF OIL GAS & MINING PRICE UTAH

Division of Oil, Gas and Mining
c/o College of Eastern Utah
451 East 400 North
Price, UT 84501

Attention: Pete Hess

RE: Sediment Pond D008 Re-certification; U.S. Fuel Company, Hiawatha Mine, Permit ACT/007/011.

Dear Pete,

Attached is the certified drawing for sediment pond D008 which was cleaned out in December 1995. The decant pipe has not been re-assembled due to the frozen ground, but will be as soon as conditions allow. Location of the end of the pipe will have to be surveyed.

Please give us a phone call if you have any questions.

Sincerely,

Mike Watson
President

POND D008

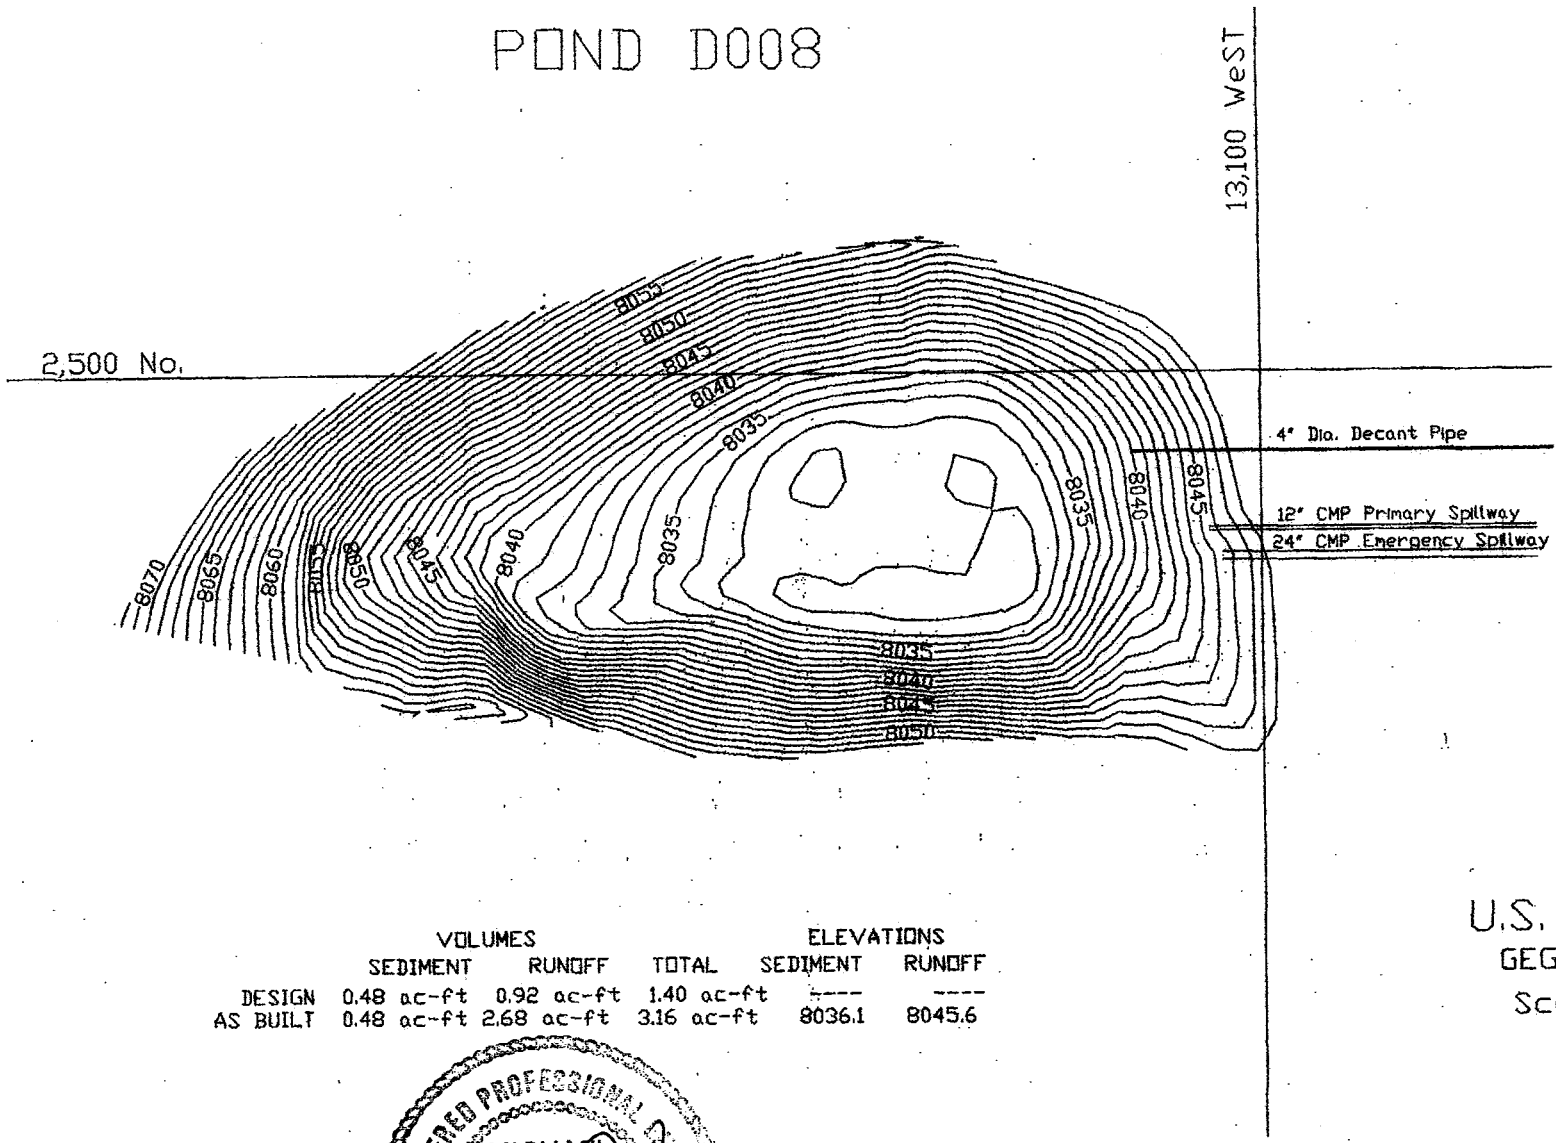

ELEV	AREA (sqft)	CUMULATIVE VOLUME (acft)
8031	0	0.00
8032	1186	0.01
8033	3994	0.07
8034	5143	0.18
8035	6167	0.31
8036	7201	0.46
8037	8245	0.64
8038	9305	0.84
8039	10370	1.07
8040	11402	1.32
8041	12418	1.59
8042	13423	1.89
8043	14479	2.21
8044	15607	2.55
8045	16791	2.92
8045.6	17560	3.16
8046	18073	3.32
8047	19439	3.75
8048	20933	4.22

U.S. Fuel Co.

GEG 1/8/96

Scale: 1" = 50"

	VOLUMES			ELEVATIONS	
	SEDIMENT	RUNOFF	TOTAL	SEDIMENT	RUNOFF
DESIGN	0.48 ac-ft	0.92 ac-ft	1.40 ac-ft	----	----
AS BUILT	0.48 ac-ft	2.68 ac-ft	3.16 ac-ft	8036.1	8045.6

REGISTERED PROFESSIONAL ENGINEER
MICHAEL P. WATSON
7055
STATE OF UTAH
